

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



SECOND MEETING OF STEERING COMMITTEE OF PMU FOR HEWP ON 28.01.2025 AT 11:00 AM

From

The Project Director,
Haryana Engineering Works Portal (HEWP),
-cum-Chief Engineer (Rural),
O/o Engineer-in-Chief, Haryana,
Public Health Engineering Department,
Panchkula.

To

- 1. The Engineer-in-Chief, Haryana PW (B&R) Department
- The Engineer-in-Chief, Haryana Public Health Engineering Department
- 3. The Engineer-in-Chief, Haryana Irrigation & Water Resources Department
- The Engineer-in-Chief, Haryana State Agriculture Marketing Board Panchkula
- The Chief Engineer, Development and Panchayat Department, Haryana
- The Chief Engineer, Urban Local Bodies Department, Haryana
- 7. The Chief Engineer, Haryana State Industrial and Infrastructure Development Corporation
- The Chief Engineer, Faridabad Metropolitan Development Authority
- The Chief Engineer, Gurugram Metropolitan Development Authority
- The Chief Engineer, Haryana Police Housing Corporation Limited
- 11. The Chief Engineer, Haryana School Shiksha Pariyojna Parishad
- 12. The Chief Engineer, Housing Board, Haryana
- The Chief Engineer, Haryana Shehri Vikas Pradhikaran



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



- 14. The Chief Engineer (PD & C), Haryana Vidyut Prasaran Nigam Limited
- The Chief Engineer (PD & C), Uttar Haryana Bijli Vitran Nigam Limited
- 16. The Chief Engineer (PD & C),
 Dakshin Haryana Bijli Vitran Nigam Limited
- 17. The Chief Engineer (Admin.),
 Haryana Power Generation Corporation Limited
- 18. The Chief Engineer,
 Micro Irrigation & Command Area Development Authority, Haryana
- 19. The Principal Director, Haryana Irrigation Research and Management Institute
- 20. The Managing Director, Haryana State Roads and Bridges Development Corporation

Memo No. 5409 - 5428 /HEWP

Dated: 21 01 2025

Subject:

Second Meeting of the Steering Committee of Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP to be held under the Chairmanship of the Commissioner & Secretary to Govt. Haryana PHE Department on 28.01.2025 at 11:00 AM.

The second meeting of the Steering Committee of the Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP would be held under the Chairmanship of Commissioner & Secretary to Govt. Haryana, Public Health Engineering Department on 28.01.2025 at 11:00 AM in the Conference Hall of Haryana PHE Department, Bays No. 19-20, Sector-4, Panchkula. The Agenda of the meeting is enclosed.

I have been directed to request you to attend the meeting on the scheduled date & time.

DA / Agenda

Project Engineer HEWP for Project Director HEWP



Bays No. 13-18, Sector 4, Panchkula - 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Endst. No. 5429

/HEWP

Dated: 21 01 2025

A copy of above is forwarded to the Director General, Supplies & Disposals Department, Haryana with request to attend the meeting on the scheduled date & time with reference to Item No. 1/3 of the Agenda Item No. 2/1.

DA/ Agenda

for Project Director HEWP

Endst. No. 5430

/HEWP

Dated: 21|01|2025

A copy is forwarded to OSD to the Commissioner & Secretary to Govt. Haryana Public Health Engineering Department for kind information of the Officer please.

DA/ Agenda

Project Engineer HEWP for Project Director HEWP

Haryana Engineering Works Portal Public Health Engineering Department, (PHED), Haryana



Agenda of the 2nd Meeting

of the

Steering Committee

of

PMU for Development & Maintenance of HEWP

To be held on :- 28.01.2025

Time :- 11:00 AM

Venue :- Conference Hall of O/o Engineer-in-Chief,

Haryana PHE Deptt., Bay No. 19-20,

Sector - 4 Panchkula

Prepared By:Project Director

Haryana Engineering Works Portal

Agenda for second Meeting of Steering Committee

of

PMU for Development & Maintenance of HEWP

INDEX

Sr.	Agenda Item No.	Description of Items	Page No
No.			
1	Agenda Item No. 2/1.	Confirmation of the Proceedings of the first meeting held on 20.12.2023	1
2	Agenda Item No. 2/2.	Action Taken Report on the decisions taken in the 1st meeting of the Steering Committee held on 20.12.2023	2
3	Agenda Item No. 2/3.	Departments/ Boards/ Corporations/ Universities etc. on-boarded on HEW Portal	6
4	Agenda Item No. 2/4.	Key statistics of HEWP	6
5	Agenda Item No. 2/5.	Department-Wise Progress of works on HEWP	6
6	Agenda Item No. 2/6.	Contractor Works pending for Scoring	7
7	Agenda Item No. 2/7.	Integration of Banks with HEWP	7
8	Agenda Item No. 2/8.	Registration-cum-Enlistment Rules for Contractors	8
9	Agenda Item No. 2/9.	Proposed changes in Common Bid Document (CBD)	8
10	Agenda Item No. 2/10.	New Modules in Development	10
11	Agenda Item No. 2/11.	Impact of Offline Bill Processing on Work Closure and Bid Capacity Scoring	11
12	Agenda Item No. 2/12	GST Reimbursement Bills	12
13	Agenda Item No. 2/13	Ticket Resolution Status and Training/Feedback Sessions on HEW Portal	13
14	Agenda Item No. 2/14	Final Bill Submission Time Limit for Contractors after expiry of Agreement	14

Details of Annexures:-

Sr. No.	Details of Annexures	Page No.
1	Annexure 'A' (Proceedings of the First meeting of Steering Committee of PMU of HEWP circulated vide Project Director HEWP Memo No. 13696-13715/HEWP dated 05/02/2024)	15-25
2	Annexure 'B' (List of Govt. Departments, Boards, Corporations and Universities on-boarded on HEWP)	26
3	Annexure 'C' (Latest Key Statistics of HEWP)	27
4	Annexure 'D' (Status of estimates on HEWP in respect of various Departments, Boards, Corporations, Universities etc.)	28-32
5	Annexure 'E' (Department wise details of the Contractor works pending for scoring.)	33-37
6	Annexure 'F' (Engineer-in-Chief, Haryana PHE Department Memo No. 44828-PHE/HEWP dated 14/05/2024)	38-45
7	Annexure 'G' (Engineer-in-Chief, Haryana PHE Department Memo No. 83414-PHE/HEWP dated 26/09/2024)	46
8	Annexure 'H' (Clauses proposed to be added to Common Bid Document)	47-48
9	Annexure 'I' (Dashboard of Project)	49
10	Annexure 'J'(Dashboard of Contract Agreement – One Package)	50
11	Annexure 'K' (Department wise list showing the number of works allotted and that for which E-MB/ Billing has been done on HEWP)	51-54

Agenda for the Second meeting of the Steering Committee of Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP.

.....

Haryana Engineering Works Portal (HEWP) was launched with an aim to bring in transparency, speed of execution, ease of access and doing business for contractors for engineering works being executed by various Govt. Departments/ Boards/ Corporations. It has been developed as a complete end-to-end solution to cater Contractor Registration & all the Engineering their Work Assessment and needs of executing Departments/Boards/Corporations starting from electronic Estimate preparation, Administrative approval, Technical Sanction, Detailed-Notice-Inviting-Tender (DNIT), electronic Common Bid Document, e-Tendering, Online Technical Evaluation of Bids, Objections resolution, Negotiation & Allotment of work, electronic Measurement Book, electronic Billing to Final Bill payment of the work.

Agenda Item No. 2/1: Confirmation of the Proceedings of the first meeting of the Steering Committee held on 20.12.2023.

The proceedings of first meeting of the Steering Committee of Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) held under the Chairmanship of the Additional Chief Secretary to Govt. Haryana, Public Health Engineering Department, Haryana on 20.12.2023 were circulated vide Project Director, HEWP Memo No.13696-13715/HEWP dated 05.02.2024 (**Annexure 'A'**) to all the members and the various Organizations on-boarded on HEWP. No observation has been received in this regard from any member.

Agenda is placed before the members of the Steering Committee of PMU of HEWP for confirmation of the proceedings of the first meeting of the Steering Committee.

Agenda Item No. 2/2: Action Taken Report on the decisions taken in the first meeting of the Steering Committee held on 20.12.2023.

The action taken report on various points is submitted as under:-

Item	Description of Items	Action taken
No.		
1/1	Brief Statistics of HEWP. The Committee was informed that 46 Govt. Organizations have so far been on-boarded on HEWP. The brief statistics of HEWP were also explained. The Chairman desired that the Agenda for the meeting of Apex Committee of PMU for Development & Maintenance of HEWP be also put up.	Due to two elections during the year 2024, the meeting of Apex Committee could not be held. The meeting of Apex Committee will be convened after second meeting of the Steering Committee.
1/2	SQL Server license procurement status. The procurement status of SQL Server license was informed to the Committee. The process of procurement of SQL Server license has since been completed. The SQL Server license have also been received and installed on the Server.	The action in the matter has been completed.
1/2		The proceedings of first reaction of
1/3	Opening of Bank account of HEWP. The status about opening of Bank account of HEWP was explained to the Committee. The representative of Director General, Supplies & Disposals, Haryana attended the meeting through Video Conferencing. The Chairman asked the Director General, Supplies & Disposals, Haryana to take necessary action on the directions of Hon'ble CM Haryana conveyed vide Diary No. 17224 dated 11/04/2022 regarding transfer of eservice fee collected per bid on the NIC e-Tendering Portal to the designated account of the HEWP.	The proceedings of first meeting of Steering Committee were also sent to the Director General, Supplies & Disposals Haryana vide memo no. 13696-13715/HEWP dated 05.02.2024 for information and necessary action on this point. However, no action in the matter has so far been taken by said Department.
	(Action:- Director General, Supplies Disposals)	

1/4	NIC e-Tendering integration issue.	Integration has been done and made
1/4		
	The progress made in the matter of	
	integration of NIC e-Tendering Portal with	· ·
	Haryana Engineering Works Portal was	BoQ Comparative Summary of the
	informed to the Committee. The integration	tenders floated through HEWP
	of NIC e-Tendering Portal with HEW Portal	through an API interface. The same is
	has since been done and tested successfully.	yet to be provided by NIC.
	The NIC Team has communicated that HEW	
	Portal may go live with said integration by	
	22/01/2024.	
1/5	Bank integration with HEWP.	The latest status has been updated at
	It was informed that Bank of Baroda has been	Agenda item No. 2/7.
	integrated with HEWP for payment of	,
	contractor bills of HSAMB and that the	
	process for integration of IndusInd Bank with	
	HEWP for payment of contractor bill of	
	Development & Panchayat Department has	
	been undertaken.	
	been undertaken.	
1/6	Registration-cum-Enlistment Rules for	The latest status has been updated at
1/6	Registration-cum-Enlistment Rules for contractors.	The latest status has been updated at Agenda item No. 2/8.
1/6		·
1/6	contractors.	·
1/6	contractors. The Committee was informed that the	·
1/6	contractors. The Committee was informed that the approval of the draft Registration-cum-	·
1/6	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman	·
1/6	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD	·
	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt.	Agenda item No. 2/8.
1/6	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP.	·
, and the second	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff	Agenda item No. 2/8.
	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development &	Agenda item No. 2/8.
	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff	Agenda item No. 2/8.
	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development &	Agenda item No. 2/8.
1/7	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP.	Agenda item No. 2/8. This is for information only.
1/7	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP. Redressal of Grievances on HEWP.	Agenda item No. 2/8. This is for information only.
1/7	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP. Redressal of Grievances on HEWP. The mechanism for redressal of grievances	Agenda item No. 2/8. This is for information only.
1/7	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP. Redressal of Grievances on HEWP. The mechanism for redressal of grievances related to the operation of HEWP raised by the on-boarded contractors and Govt.	Agenda item No. 2/8. This is for information only.
1/7	contractors. The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt. Staff position of PMU HEWP. The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP. Redressal of Grievances on HEWP. The mechanism for redressal of grievances related to the operation of HEWP raised by the on-boarded contractors and Govt.	Agenda item No. 2/8. This is for information only.

1/9 Allotment of Tenders in offline mode.

The Committee was informed that though the instructions issued vide worthy PSCM office note dated 23/12/2022 in the matter, allotment for the works is being made in offline mode by several Govt. Organizations. The Chairman directed that the instructions issued vide worthy PSCM note dated 23/12/2022 regarding undertaking allotment and post allotment activities on HEWP, be complied by all the Organizations on-boarded on HEWP.

The latest status has been updated at Agenda item No. 2/10.

(Action:- All Govt. Organizations onboarded on HEWP) Revision of Haryana Schedule of Rates

1/10 | Revision of Haryana Schedule of Rates.

The Committee was informed that action for revision of Haryana Schedule of Rates is being undertaken by PWD (B&R). The suggestions regarding revision of HSR-2021 were invited on HEWP and the suggestions so received have been forwarded to the Zonal Committee for further necessary action in the matter.

(Action:- PWD (B&R)

The record of discussion of meeting held under the Chairmanship of ACS PHED on 05/06/2023 regarding revision of HSR were sent vide memo 60666-67/HEWP 30/06/2023 to the Engineer-in-Chief Haryana **PWD** (B&R and the Engineer-in-Chief Haryana I&WR Department to take necessary action in the matter. The action is under process in PWD (B&R)

1/11 Offline preparation of bills of the works allotted on HEW Portal.

The Committee was informed that most of the Govt. Organizations on on-boarded on HEW Portal have not gone for E-MB and Billing on HEWP. The Chairman asked that E-MB and Billing on HEWP be implemented by all Organizations on-boarded on HEWP.

(Action:- All Govt. Organizations onboarded on HEWP) The latest status has been updated at Agenda item No. 2/7.

Other points discussed with the permission of the Chair:-

The Nodal Officer HEWP, Development & Panchayat Department raised the following issues:

- 1. Tenders are floated by the Engineering wing but the payment is made by PRI in the Development & Panchayats PRI Department and therefore representatives need to be on-boarded on HEW Portal for making the payments. The Nodal Officer was informed that the E-MB and Billing may be done on HEWP and approval regarding the exemption of payment on HEWP by the PRI may be taken from Govt.
- 2. Approval has been granted by the Finance Department for the Integration of IndusInd Bank with HEWP for payment of contractor bills. The process for integration of the IndusInd Bank may be completed at the earliest. The Nodal officer was informed that this point has already been covered in Agenda Item No. 1/5.
- 3. The Bank Account of Haryana Grameen Vikas Yojana under the Rural Development Department is being maintained in HDFC Bank which is required to be integrated with HEWP. It was decided that Rural Development Department may seek approval from the Finance Department for the integration of HDFC Bank with HEWP for payment of the Contractor Bill for this scheme.

(Action:- Rural Development Department, HEWP Team)

This is for information only.

Integration is pending at the level of IndusInd Bank. The Development & Panchayat Department may ask the bank to complete the integration at the earliest.

The proceedings of second meeting of Steering Committee were also sent to the Director General, Development & Panchayat Department Haryana vide memo no. 13696-13715/HEWP dated 05.02.2024 for information and necessary action in the matter. The reply is awaited.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/3: Departments/ Boards/ Corporations/ Universities etc. on-boarded on HEW Portal

Since its inception, 53 Govt. Departments, Boards, Corporations, Universities etc. (**Annexure 'B'**) have been on-boarded on HEWP.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/4: Key statistics of HEWP

The latest key statistics of HEWP are enclosed at **Annexure 'C'**.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/5: Department-Wise Progress of works on HEWP

The report about the status of estimates Administratively Approved and Technically Sanctioned, DNITs approved, Tenders floated and Allotments made on HEWP in respect of the various Departments, Boards, Corporations, Universities etc. is enclosed at **Annexure** 'D'.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/6: Contractor Works pending for Scoring

The scoring of works completed and submitted by Contractor through his Login is to be done by the concerned Executive Engineers/ Sub-Divisional Engineers (in case of Development & Panchayat Department only). The benefit of EMD exemption is available only to the Contactors registered on HEW Portal having a score of 70 and above for the works submitted by him. As on 07.01.2025, a total of 368 Contractor works submitted by the Contractors are pending for scoring across various Departments. Out of these, 321 works have been pending for more than 30 days. The Department-wise details of the Contractor works pending for scoring is attached at **Annexure 'E'**.

It is proposed that the respective Departments be asked to clear this pendency and ensure the scoring of Contractor works by the concerned offices in time.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/7: Integration of Banks with HEWP

The Finance Department vide U.O. No. IFCC/2022/19954 dated 21/10/2022 and U.O. No. IFCC/2022/27503 dated 20/12/2022 has authorized four banks for integration with the HEW Portal to facilitate the payment of contractor bills:

- 1. State Bank of India
- 2. Punjab National Bank
- 3. Bank of Baroda
- 4. Union Bank of India

The efforts to integrate these banks with the HEWP have been undertaken for the following departments:

Name of Govt.	Name of Bank	Status
Organization		
Haryana State	Bank of Baroda	Integration completed. The payment
Agriculture Marketing		amounting to ₹ 412 Crore has so far been
Board (HSAMB)		made by HSAMB through Bank of Baroda.

HSVP	Punjab National	Whitelisting of IP has been done and
	Bank	testing is in progress for the same.
HPHC	Union Bank of	Whitelisting of IP has been done and
	India	testing is in progress for the same.

Other departments are yet to initiate the integration process to facilitate contractor payments through the HEWP.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/8: Registration-cum-Enlistment Rules for Contractors

The draft **Registration-cum-Enlistment Rules for Contractors-2023** were prepared by PWD (B&R) and submitted for approval from Government. Subsequently, the Finance Department sought clarifications on the matter through U.O. No. 17/01/2020-3FICW/11933 dated 03/08/2023. The reply to the same has been submitted by PWD (B&R). The approval of these rules is now awaited from the Government.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/9: Proposed changes in Common Bid Document (CBD)

A letter proposing changes to the Common Bid Document (CBD) was submitted to PWD (B&R) via Memo No. 44828-PHE/HEWP dated 14.05.2024 (attached as **Annexure 'F'**). To follow up, a reminder letter was issued through Memo No. 83414-PHE/HEWP dated 26.09.2024 (attached as **Annexure 'G'**). However, no further action has been taken on the proposed changes as of now.

The following is the brief description of the above mentioned proposed changes in CBD required to address several challenges and ambiguities faced by users in the existing Common Bid Document (CBD):

- 1. *Part Shifting*: Clause 4(A) to be moved to Clause 3 (Eligible Bidders).
- 2. <u>Qualification for Works up to ₹25.00 Lacs</u>: Amendments to clarify that only a Contractor ID on the HEW Portal is mandatory, with no requirement for Registration.
- 3. *Qualification for Works from ₹25.01 to ₹64.00 Lacs*: Replace the term "Registration" with "Enlistment Certificate" to avoid confusion.
- 4. Award of Contract Criteria: Amendments for better alignment with current practices.
- 5. <u>Prime Contractor Criteria</u>: Changes in Qualification Information for works performed as Prime Contractor.
- 6. <u>Technical Conditions</u>: Amendments specific to Electrical and Instrumentation (EI) works.
- 7. <u>Maintenance Contract Conditions</u>: Deletion of Point No. 7 in Additional Conditions for Maintenance Contracts.
- 8. <u>Integrity Pact Format</u>: Clarify submission requirements to resolve contradictions between Page 323, which mandates submission with technical bids, and Clause 36.2 on Page 34, which requires signing by the successful bidder.

These proposed changes aim to enhance clarity and reduce confusion in the CBD, facilitating smoother operations for users.

Besides these, the new Clauses regarding Termination of Contract on Death of Contractor (Proprietorship Firm) and Provisions for Death of Partner/Director are also proposed to be added to the CBD. Details of these proposed Clauses are attached as Annexure 'H' for reference.

The addition of the above Clauses aim to establish a clear framework for addressing such situations and ensuring smooth continuity in the firm's or company's operations.

This is for the information and consideration of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/10: New Modules in Development

The development of several new modules is underway, aimed at enhancing the functionality and user experience on the HEW Portal. The following key modules are currently under development:

- 1. <u>Dashboard of Project (Annexure I)</u> will provide a centralized location for all project-related information. It will allow users to access important details, such as project beneficiary information, key timelines, and additional relevant data in one place. This dashboard will enable the monitoring of multiple project packages from a single platform. Users will be able to explore each package in further detail by clicking on them. Additionally, the dashboard will feature details of key project staff and their roles, along with information on approved and pending permissions from various departments required for the project's execution.
- 2. <u>Dashboard of Contract Agreement (One Package) (Annexure J)</u> will provide a more detailed view of individual project packages. Upon clicking on a package, users will be redirected to the contract agreement dashboard. This dashboard will display key project timelines and the current status of the project, providing authorities with an easy way to track progress. It will also allow for monitoring key performance indices, milestones, and a comparison of planned versus actual progress, along with a graphical representation of the project timeline.
- 3. Integration of the Bid Capacity Formula on the HEW Portal: This development will allow for better tracking and analysis of contractors' capabilities by integrating the Bid Capacity Formula directly into the HEW Portal, providing an efficient way to assess contractors' qualifications and project suitability.
- 4. <u>Milestone-Based System & Process for Contractor Actions</u>: A Milestone-Based System will be implemented to ensure projects are tracked according to predefined

milestones, improving project monitoring and for imposing Liquidated Damages for the delay of work as per CBD provision.

Additionally, the portal will integrate the process for **Debarring/Blacklisting/Demotion to Lower Class/Deregistration of Contractors**, along with an appeal procedure. This will promote transparency and accountability in contractor management, ensuring efficient decision-making and streamlined processing of contractor-related actions.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/11: Impact of Offline Bill Processing on Work Closure and Bid Capacity Scoring

The HEW Portal is designed to ensure that works completed by contractors in 2024 are automatically included in the "Work Experience" section for accurate bid capacity calculations. To facilitate this, the system restricts the concerned competent authority, who approves the final bill, from closing the work without assigning a score to the contractor's performance.

However, it has been observed that: several Departments are still processing contractor bills offline instead of using the online billing system. The Department wise list showing the number of works allotted and the number of works for which E-MB/ Billing has been done on HEWP (**Annexure-K**) reveals the detail of such Departments.

This offline processing of bills is creating the following challenges:

- 1. <u>Work Closure Restrictions</u>: Competent authorities are unable to assign performance scores for contractors' completed works due to the lack of online records.
- 2. <u>Impact on Bid Capacity</u>: Contractors are unable to upload their completed works for 2024 on the HEW Portal, resulting in inaccurate bid capacity calculations.

It is proposed that all departments currently processing bills offline may be asked to adopt the online billing system without delay. Transitioning to online bill processing will resolve the above issues, ensure accurate work experience records on the HEW Portal, and prevent negative impacts on Contractors' Bid Capacity.

This is for the information and consideration of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/12: GST Reimbursement Bills

An issue was raised by the Chief Engineer, Development & Panchayat Department, regarding the payment of GST reimbursement bills to contractors.

In response, the Project Director of the Haryana Engineering Works Portal (HEWP) clarified that payments for GST reimbursements must be processed in accordance with **Clause 13.4 of the Common Bid Document (CBD)**, which states:

"All duties, taxes (excluding GST), royalties, compensation, costs, and other levies payable by the Contractor under the Contract or for executing the item(s) of work or any other cause, shall be included in the rates, prices, and total Bid price submitted by the Bidder online. The GST amount shall be reimbursed upon production of proof of GST deposit with the Government for the previous payment".

It is proposed that in order to ensure smooth and compliant processing of GST reimbursement bills, it is recommended that all departments be directed to follow the guidelines outlined in Clause 13.4 of the Common Bid Document (CBD). Specifically, departments should ensure that the GST reimbursement is processed only upon submission of valid proof of GST deposit by the contractor. Clear instructions should be issued to all departments to ensure uniformity and compliance, thereby facilitating timely and accurate reimbursement payments.

This is for the information and consideration of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/13: Ticket Resolution Status and Training/Feedback Sessions on HEW Portal

As of 07.01.2025, a total of 30,856 tickets have been received on the HEW Portal. The current resolution status is as follows:

- > **30,620 Tickets** have been successfully closed, demonstrating the efficiency of the portal's issue resolution process.
- > The remaining **236 Tickets** are currently being processed by the concerned teams.

Training Sessions on HEW Portal Modules:

In parallel with resolving tickets, 19 training sessions have been conducted on the HEW Portal's modules since 01.03.2024. These sessions aim to enhance the understanding of portal functionalities among department officials and contractors.

- **14 sessions** were conducted through **Video Conferencing**, ensuring broader participation from different locations.
- **5 sessions** were held **offline**, providing more focused, hands-on training.

Feedback and Q&A Sessions:

To complement the training, Feedback and Q&A sessions have been conducted to address user queries and gather input for future improvements to the portal. These sessions have played a key role in reducing the number of tickets related to portal usage and have significantly enhanced the portal's overall effectiveness.

Registration for Training Sessions:

Both department officials and contractors interested in attending training sessions on any HEW Portal module can easily register by following the steps outlined in the User Manual "Module Training Request" which is available under User Manual Tab (Download>>User Manual) on home page and also available under the "What's New" section on both the department and contractor logins for easy access.

This is for the information of the members of the Steering Committee of PMU of HEWP please.

Agenda Item No. 2/14: Final Bill Submission Time Limit for Contractors after expiry of Agreement

The timeline for contractors to submit their final bills, after the expiry of an agreement, was discussed during the meeting held on 19.04.2024 under the chairmanship of the Engineer-in-Chief (Roads), PWD (B&R), in the Main Committee Room, Nirman Sadan, Plot No. 1, Sector-33/A, Chandigarh. During the meeting, it was decided that contractors would have 60 days from the expiry of their agreement to submit their final bills. Following the discussion, a system check was implemented to enforce this timeline as per which, contractors are required to submit their final bill within the 60-day period post-agreement expiry. If a contractor fails to meet this deadline, they must apply for a time extension through the HEW Portal. This extension must be approved by the concerned competent authority. Without such approval, the contractor will not be able to submit their final bill.

It is proposed that the 60-day timeline for contractors to submit their final bills post-agreement expiry, or another suitable timeline, be formally finalized and adopted. Clear instructions should be issued to all departments to ensure strict adherence to this timeline. Contractors should be informed that, if they are unable to submit their final bill within the specified period, they must apply for a time extension through the HEW Portal. This extension will be subject to approval by the concerned competent authority. This measure will ensure uniformity and facilitate the timely submission of final bills across all departments.

This is for the information and consideration of the members of the Steering Committee of PMU of HEWP please.

Any other item with the permission of Chair.



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



From

The Project Director,
Haryana Engineering Works Portal (HEWP),
-cum- Chief Engineer (Mech.),
O/o Engineer-in-Chief, Haryana,
Public Health Engineering Department,
Panchkula.

To

- The Engineer-in-Chief, Haryana PW (B&R) Department.
- The Engineer-in-Chief, Haryana Public Health Engineering Department.
- 3. The Engineer-in-Chief, Haryana Irrigation & Water Resources Department.
- Engineer-in-Chief, Haryana State Agriculture Marketing Board Panchkula
- The Chief Engineer, Development and Panchayat Department
- The Chief Engineer, Urban Local Bodies Department
- 7. The Chief Engineer, Haryana State Industrial and Infrastructure Development Corporation
- 8. The Chief Engineer, Faridabad Metropolitan Development Authority
- The Chief Engineer, Gurugram Metropolitan Development Authority
- The Chief Engineer, Haryana Police Housing Corporation Limited
- The Chief Engineer, Haryana School Shiksha Pariyojna Parishad
- The Chief Engineer, Housing Board Haryana
- 13. The Chief Engineer, Haryana Shehri Vikas Pradhikaran
- The Chief Engineer (PD & C), Haryana Vidyut Prasaran Nigam Limited
- The Chief Engineer (PD & C), Uttar Haryana Bijli Vitran Nigam Limited



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



- The Chief Engineer (PD & C),
 Dakshin Haryana Bijli Vitran Nigam Limited
- The Chief Engineer (Admin.),
 Haryana Power Generation Corporation Limited
- The Chief Engineer,
 Micro Irrigation & Command Area Development Authority Haryana
- Principal Director, Haryana Irrigation Research and Management Institute
- 20. The Managing Director,
 Haryana State Roads and Bridges Development Corporation

Memo No. 13696-13715 /HEWP Dated: 05 | 02 | 24

Subject:

Proceedings of First Meeting of the Steering Committee of PMU for Development & Maintenance of HEWP held on 20.12.2023 at 12:30 PM under the Chairmanship of worthy Additional Chief Secretary to Govt. Haryana PHE Department.

Please find enclosed herewith the Proceedings of First Meeting of the Steering Committee of the Project Management Unit (PMU) for Development & Maintenance of Haryana Engineering Works Portal (HEWP) held on 20.12.2023 at 12:30 PM under the Chairmanship of worthy Additional Chief Secretary to Govt. Haryana PHE Department for information a necessary action.

DA / Proceedings of meeting.

Project Engineer HEWP for Project Director HEWP

Endst. No. 13716

/HEWP

Dated: 05/02/24

A copy is forwarded to the Director General, Supplies & Disposals, Haryana for information and necessary action with reference to Item No. 1/3 of the Proceedings.

DA/ Proceedings of meeting.

Project Engineer HEWP for Project Director HEWP

Endst. No. 13717 - 13742

/HEWP

Dated: 05 02 24

A copy is forwarded to the following for information and necessary action:

- The Managing Director, Haryana State Cooperative Supply and Marketing Federation Limited
- The Managing Director, Haryana State Warehousing Corporation
- The Managing Director, Haryana Tourism Corporation Limited



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



- The Director General, Haryana Renewable Energy Development Agency
- 5. The Director, Agriculture and Farmer Welfare Department
- The Chief Executive Officer, Faridabad Smart City
- 7. The Director, Fisheries Department
- The Principal Chief Conservator of Forest, Forest Department
- The Managing Director, Haryana State Co-operative Labour & Construction Federation Limited
- The Chief Executive Officer, Panchkula Metropolitan Development Authority
- The Chief Executive Officer, Shri. Mata Mansa Devi Shrine Board, Panchkula
- The Director, Skill Development and Industrial Training Department
- The Director General, Horticulture Department, Haryana
- The Director, Local Audit Department, Haryana
- The Vice Chancellor, Choudhary Charan Singh Haryana Agricultural University Hisar
- The Vice Chancellor, Deen Bandhu Chootu Ram University of Science & Technology, Murthal
- The Vice Chancellor, Kurukshetra University, Kurukshetra
- The Vice Chancellor, Maharana Pratap Horticulture University, Karnal
- The Vice Chancellor, Chaudhary Bansi Lal University, Bhiwani
- The Vice Chancellor, Chaudhary Ranbir Singh University, Jind
- 21. The Vice Chancellor,
 Guru Jambheshwar University of Science and Technology, Hisar
- The Vice Chancellor, Gurugram University, Gurugram
- 23. The Vice Chancellor, Indira Gandhi University, Meerpur, Rewari



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



24. The Vice Chancellor, Maharashi Dayanand University, Rohtak

25. The Vice Chancellor, Shri Vishwakarma Skill University

26. The Vice Chancellor, YMCA Technical University, Faridabad

DA/ Proceedings of meeting.

Project Engineer HEWP for Project Director HEWP

Endst. No. 13743 CFMS No. 929

/HEWP

Dated: 05/02/24

A copy is forwarded to PS to Additional Chief Secretary to Govt. Haryana Public Health Engineering Department for the kind information of worthy ACS PHED.

DA/ Proceedings of meeting.

Project Engineer HEWP for Project Director HEWP



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Proceedings of First meeting of the Steering Committee of PMU for Development & Maintenance of HEWP held on 20.12.2023 at 12:30 PM under the Chairmanship of worthy Additional Chief Secretary to Government of Haryana, PHE Department.

The First meeting of the Steering Committee of PMU for Development & Maintenance of HEWP was held on 20.12.2023 at 12:30 PM under the chairmanship of worthy ACS PHED at VC Room, Ground Floor, Mini Secretariat, Sector-17, Chandigarh.

Participants:

Attendance sheet of the members who participated physically is attached as Annexure- I. The list of members and participants who attended the meeting through Video Conferencing is attached at Annexure- II.

The Project Director, Haryana Engineering Works Portal welcomed ACS, PHED and other members of Steering Committee to the First Meeting of the Steering Committee of PMU for Development & Maintenance of HEWP. At the outset, agenda of meeting and a brief presentation was placed before the quorum. The Project Director HEWP explained all the agenda points to the quorum as per agenda sequences.

Agenda wise proceedings of the meeting are as under:-

Item No. 1/1: Brief Statistics of HEWP.

The Committee was informed that 46 Govt. Organizations have so far been on-boarded on HEWP. The brief statistics of HEWP were also explained. The Chairman desired that the Agenda for the meeting of Apex Committee of PMU for Development & Maintenance of HEWP be also put up.

Item No. 1/2: SQL Server license procurement status.

The procurement status of SQL Server license was informed to the Committee. The process of procurement of SQL Server license has since been completed. The SQL Server license have also been received and installed on the Server.

Item No. 1/3: Opening of Bank account of HEWP.

The status about opening of Bank account of HEWP was explained to the Committee. The representative of Director General, Supplies & Disposals, Haryana attended the meeting through Video Conferencing. The Chairman asked the Director General, Supplies & Disposals, Haryana to take necessary action on the directions of Hon'ble CM Haryana conveyed vide Diary No. 17224 dated 11/04/2022 (Annexure – III) regarding transfer of e-service fee collected per bid on the NIC e-Tendering Portal to the designated account of the HEWP.

(Action:- Director General, Supplies & Disposals)



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Item No. 1/4:

NIC e-Tendering integration issue.

The progress made in the matter of integration of NIC e-Tendering Portal with Haryana Engineering Works Portal was informed to the Committee. The integration of NIC e-Tendering Portal with HEW Portal has since been done and tested successfully. The NIC Team has communicated that HEW Portal may go live with said integration by 22/01/2024.

Item No. 1/5:

Bank integration with HEWP.

It was informed that Bank of Baroda has been integrated with HEWP for payment of contractor bills of HSAMB and that the process for integration of IndusInd Bank with HEWP for payment of contractor bill of Development & Panchayat Department has been undertaken.

(Action:- Development & Panchayat Department, HEWP Team)

Item No. 1/6:

Registration-cum-Enlistment Rules for Contractors.

The Committee was informed that the approval of the draft Registration-cum-Enlistment Rules-2023 prepared by PWD (B&R) is awaited from Govt. The Chairman asked the Engineer-in-Chief PWD (B&R) to follow the matter with Govt.

(Action:-PWD (B&R))

Item No. 1/7:

Staff position of PMU HEWP.

The Committee was informed about the staff position of the PMU for the Development & Maintenance of HEWP.

Item No. 1/8:

Redressal of Grievances on HEWP.

The mechanism for redressal of grievances related to the operation of HEWP raised by the on-boarded contractors and Govt. Organizations was explained to the Committee.

Item No. 1/9:

Allotment of Tenders in offline mode.

The Committee was informed that though the instructions issued vide worthy PSCM office note dated 23/12/2022 (Annexure- IV) in the matter, allotment for the works is being made in offline mode by several Govt. Organizations. The Chairman directed that the instructions issued vide worthy PSCM note dated 23/12/2022 regarding undertaking allotment and post allotment activities on HEWP, be complied by all the Organizations on-boarded on HEWP.

(Action:- All Govt. Organizations on-boarded on HEWP)



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Item No.1/10:

Revision of Haryana Schedule of Rates.

The Committee was informed that action for revision of Haryana Schedule of Rates is being undertaken by PWD (B&R). The suggestions regarding revision of HSR-2021 were invited on HEWP and the suggestions so received have been forwarded to the Zonal Committee for further necessary action in the matter.

(Action:- PWD (B&R))

Item No.1/11:

Offline preparation of bills of the works allotted on HEW

Portal.

The Committee was informed that most of the Govt. Organizations on on-boarded on HEW Portal have not gone for E-MB and Billing on HEWP. The Chairman asked that E-MB and Billing on HEWP be implemented by all Organizations on-boarded on HEWP.

(Action:- All Govt. Organizations on-boarded on HEWP)

Other points discussed with the permission of the Chair:-

The Nodal Officer HEWP, Development & Panchayat Department raised the following issues :

- 1. Tenders are floated by the Engineering wing but the payment is made by PRI in the Development & Panchayats Department and therefore PRI representatives need to be on-boarded on HEW Portal for making the payments. The Nodal Officer was informed that the E-MB and Billing may be done on HEWP and approval regarding the exemption of payment on HEWP by the PRI may be taken from Govt.
- 2. Approval has been granted by the Finance Department for the Integration of IndusInd Bank with HEWP for payment of contractor bills. The process for integration of the IndusInd Bank may be completed at the earliest. The Nodal officer was informed that this point has already been covered in Agenda Item No. 1/5.
- 3. The Bank Account of Haryana Grameen Vikas Yojana under the Rural Development Department is being maintained in HDFC Bank which is required to be integrated with HEWP. It was decided that Rural Development Department may seek approval from the Finance Department for the integration of HDFC Bank with HEWP for payment of the Contractor Bill for this scheme.

(Action:- Rural Development Department, HEWP Team)

The meeting	ended	with	a vote	of	thanks	to	the	Chair	and	all	present	



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Annexure-I

Attendance (the members who participated physically) of First Meeting of the Steering Committee of PMU for Development & Maintenance of HEWP State held on 20.12.2023 at 12:30 PM under the Chairmanship of Sh. A. K. Singh, IAS, Additional Chief Secretary to Govt. Haryana, PHE Department, in VC Room, Ground Floor, Mini Secretariat, Sector-17, Chandigarh.

Sr. No.	Name	Designation	Mobile & E-mail ID
1.	Sh. Asheim Khanna	Engineer-in-Chief, PHED, Haryana	9416070727
2.	Sh. Mahesh Kumar Madan	Engineer-in-Chief, (Buildings)-HOD PWD (B&R)	9463999724
3.	Sh. Rajeev Yadav	Engineer-in-Chief, (Roads) PWD (B&R)	9868113500
4.	Sh. Anil Kumar Dahiya	MD, HSRDC	9417702442
5.	Sh. Rajiv Batish	Project Director, HEWP-cum-Chief Engineer (Mech.), PHED	9872617131
6.	Sh. Atul Pasrija	Chief Engineer, DHBVN	9671022240
7.	Sh. Harish Pant	SE (Construction), UHBVN	9023726614
8.	Sh. Vivek Singh	SE (HQ), ULB	7988669791
9.	Sh. Vikas Kaushik	Manager Finance, HPHC	814644141
10.	Sh. Pankaj Kamboj	Project Engineer, HEWP	9416550881
11.	Sh. Naveen Bansal	System Executive Officer, PHED	9416680242



Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172 2564083 Email: info-hewp.pwd@hry.gov.in



Annexure-II

The list of members and participants who attended, through Video Conferencing, First Meeting of the Steering Committee of PMU for Development & Maintenance of HEWP State held on 20.12.2023 at 12:30 PM under the Chairmanship of Sh. A. K. Singh, IAS, Additional Chief Secretary to Govt. Haryana, PHE Department, in VC Room, Ground Floor, Mini Secretariat, Sector-17, Chandigarh.

Sr. No.	Name	Designation
1.	Sh. Rakesh Chauhan	Engineer-in-Chief, I & WR, Haryana
2.	Sh. Kuldeep Singh	Chief Engineer, HSAMB
3.	Sh. Arun Pandey	HOD (Engg.), HSIIDC
4.	Sh. Rajesh Bansal	Chief Engineer, GMDA
5.	Sh. Vishal Bansal	Chief Engineer, FMDA
6.	Sh. Rajeev Sharma	Chief Engineer, Housing Board Haryana
7.	Sh. Suresh Kumar Yadav	Chief Engineer, MICADA
8.	Sh. M.L. Singla	Chief Engineer, HPGCL
9.	Sh. Anant Singh	SE, Civil Design, HVPNL
10.	Sh. Mandeep Singh	EE, Supplies & Disposals Department
11.	Sh. Veenus Nathalia	EE, Development & Panchayat Department
12.	Sh. Amit Rathi	EE, HSVP
13.	Sh. Bhupinder Singh	EE, HSSPP
14.	Sh. Parveen Kumar	EE, HPGCL
15.	Sh. Vikram Singh	EE, GMDA
16.	Sh. Mandeep Kumar	EE, HVPNL
17.	Sh. Naresh Sandhu	SDO, SVSU Palwal
18.	Sh. Satish Gupta	Consultant, Development & Panchayat Department



O/o EIC, PHED खाणा सरकार

A new State level portal viz., Haryana Engineering Works Portal (HEWP) is now in place as an end-to-end platform for all civil engineering works. CM has directed that the e-service fee collected per bid on the NIC e-tendering portal and currently being transferred to the 'Society for IT initiative funds for e-Governance' shall henceforth be transferred to a designated account of the HEWP. He has desired that requisite action for the same be undertaken immediately and the funds so collected in the HEWP account be utilized for expenditure on activities related to the functioning of HEWP.

ACS (Finance)

ACS (IT)

ACS (PHED)

11.04.2022

Umashankar

SELRI

25/4

24

roum maryana Diary No (F.R.)



हरियाणा सरकार

It has come to notice that departments and Government agencies are using Haryana Engineering Works (HEW) portal to prepare estimates and accord administrative approval for engineering works but allotment and post allotment activities are being carried out through an offline mode. Hon'ble CM has directed that allotment of all engineering works and post-allotment action including filling of MB, processing of bills, pre-audit of bills in case of Panchayati Raj Institutions and Urban Local Bodies and payments should also be undertaken on the HEW portal only and not through the offline mode. Finance Department has been instructed not to release payments for engineering works to be allotted on or after 26.12.2022 where allotment of works or post allotment actions are carried out through the offline mode.

(V.Umashankar)
PSCM
23.12.2022

ACS D&P
ACS ULB & TCP
MD HPHC
EIC PWD
EIC PHED
EIC Irrigation

8+ (ot/1+(ot/6)019, +3012, 2018

CC: MD HSIIDC

MD HVPN

CA HSVP

CA Housing Board

DG D&P

Director ULB

cc: ACS Finance (for taking further action to give effect to the direction of Hon'ble CM)

Director Local Audit

GOVERNMENT OF HARYANA Beti Bachao-Beti Padhao

7

Government Organizations on-boarded on HEWP

• Since its inception in May 2021, the following **53 Government Departments, Boards, Corporations and Universities** have been on-boarded on HEWP.

S	Govt. Organization Name
No	
1	Agriculture and Farmer Welfare Deptt.
2	Bhagat Phool Singh Mahila Vishwavidyalaya, Khanpur Kalan, Sonepat
3	Chaudhary Bansi Lal University, Bhiwani
4	Chaudhary Ranbir Singh University, Jind
5	Chaudhary Charan Singh Haryana Agriculture
	University, Hisar
6	Chaudhary Devi Lal University, Sirsa
7	Dakshin Haryana Bijli Vitrain Nigam Ltd.
8	Deen Bandhu Chootu Ram University of Science
	& Technology, Murthal
9	Development and Panchayat Deptt.
10	Faridabad City Transport Services Ltd.
11	Faridabad Metropolitan Development Authority
12	Faridabad Smart City
13	Fisheries Deptt.
14	Forest Deptt.
15	Guru Jambheshwar University of Science and Technology, Hisar
16	Gurugram Metropolitan Development Authority
17	Gurugram University, Gurugram
18	Haryana Irrigation Research and Management Institute
19	Haryana Police Housing Corporation Ltd.
20	Haryana Power Generation Corporation Ltd.
21	Haryana Renewable Energy Development Agency
22	Haryana Rural Development Fund Administration Board
23	Haryana School Shiksha Pariyojna Parishad
24	Haryana Shehri Vikas Pradhikaran
25	Haryana State Agriculture Marketing Board Panchkula
26	Haryana State Co-operative Labour & Construction Federation Ltd.
27	Haryana State Co-operative Supply & Marketing Federation Ltd.

0.51	
S No	Govt. Organization Name
28	Harvana State Boads and Bridges
20	Haryana State Roads and Bridges Development Corporation
29	Haryana State Warehousing Corporation
29	Trai yana State Warenousing Corporation
30	Haryana Tourism Corporation Ltd.
31	Haryana Vidyut Prasaran Nigam Ltd.
32	Horticulture Deptt.
33	Housing Board Haryana
34	Haryana State Industrial and Infrastructure
	Development Corporation
35	Indira Gandhi University, Meerpur, Rewari
36	Irrigation and Water Resources Deptt.
37	Kurukshetra University, Kurukshetra
38	Lala Lajpat Rai University (LUVAS), Hisar
39	Local Audit Department Haryana
40	Maharana Pratap Horticulture University, Karnal
41	Maharashi Dayanand University, Rohtak
42	Micro Irrigation & Command Area
	Development Authority, Haryana
43	Municipal Corporation/Urban Local Bodies
44	Panchkula Metropolitan Development Authority
45	Pandit Lakhmi Chand State University of Performing & Visual Arts, Sirsa
46	Public Health Engineering Department
47	Public Works (B&R) Department
48	Shri Mata Mansa Devi Shrine Board, Panchkula
49	Shri. Vishwakarma Skill University
50	Skill Development and Industrial Training Department
51	Sonipat Metropolitan Development Authority
52	Uttar Haryana Bijli Vitran Nigam Limited
53	YMCA Technical University, Faridabad

Key Statistics of HEWP

Particulars	
Number of on-boarded Contractors	18,124
Number of Registered Contractors	5312
Number of Approved Estimates	81,711
Amount of Approved Estimates	Rs. 81,440 Cr.
Number of Tenders Floated	67,852
Amount of Tenders Floated	Rs. 53,852 Cr.
Number of Works Allotted	55,068
Amount of Works Allotted	Rs. 21,885 Cr.

Statistics as on 07/01/2025

Entries of Capital Works in Estimate/DNIT/Tender/Allotment Modules												
		Estimate			Pa	Ten	der	Allotment				
Sr. No.	Department Nodal Officer Contact No.	A/A Approved	Tech. Not Sanctioned	Tech. Sanctioned	Packages in the Tech. Sanctioned Estimate	for which DNIT not		Approved DNIT	Yet to be Floated	Floated	Yet to be Allotted	
	Total	81711	2748	78963	81055	4424	76631	70176	2324	67852	12784	55068
1	Agriculture and Farmer Welfare Department Dr. Devinder Sihag, JD 9416380656	<u>110</u>	<u>6</u>	<u>104</u>	<u>104</u>	<u>6</u>	<u>98</u>	<u>98</u>	<u>2</u>	<u>96</u>	21	<u>75</u>
2	Bhagat Phool Singh Mahila Vishwavidyalaya, Khanpur Kalan, Sonepat	0	0	0	0	0	0	0	0	0	0	0
3	Chaudhary Bansi Lal University, Bhiwani Sh. Dinesh Kumar Madan, Professor 8199932069	<u>8</u>	0	<u>8</u>	8	0	8	8	0	<u>8</u>	<u>5</u>	<u>3</u>
4	Chaudhary Charan Singh Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313	<u>58</u>	<u>8</u>	<u>50</u>	<u>54</u>	18	<u>36</u>	28	0	28	18	10
5	Chaudhary Devi Lal University, Sirsa Sh. Rakesh Kumar, EE 9896323322	0	0	0	0	0	0	0	0	0	0	0
6	Chaudhary Ranbir Singh University, Jind Sh. Jasvir Singh, Associate Professor 9466778222	<u>9</u>	0	9	9	0	9	9	2	7	3	4
7	Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530	<u>409</u>	<u>10</u>	<u>399</u>	392	12	380	342	<u>11</u>	331	<u>273</u>	<u>58</u>
8	Deen Bandhu Chootu Ram University of Science & Technology, Murthal Vijay Kumar 9416232747	<u>15</u>	<u>4</u>	<u>11</u>	8	8	0	0	0	0	0	0
9	Development and Panchayat Sh. Veenus Nathalia, EE 9356925623	33662	315	33347	33408	<u>596</u>	32812	<u>29199</u>	1028	28171	<u>1569</u>	26602
10 28	FARIDABAD CITY TRANSPORT SERVICES	0	0	0	0	0	0	0	0	0	0	0

	Arbind Kumar 8510005801											
11	Faridabad Metropolitan Development Authority (FMDA) Sh. Ankit Bhardwaj, EE 9990606765	<u>191</u>	3	188	182	<u>19</u>	<u>163</u>	<u>163</u>	<u>6</u>	<u>157</u>	<u>60</u>	97
12	Faridabad Smart City Sh. Gyan Prakash Wadhwa, DGM(Engg) 9711876119	<u>11</u>	0	11	11	1	<u>10</u>	<u>10</u>	<u>1</u>	9	9	0
13	Fisheries Sh. Surinder Pal 9466620706	0	0	0	0	0	0	0	0	0	0	0
14	Forests Sh. Rajesh Rana, DFO(HQ) 9417401427	0	0	0	0	0	0	0	0	0	0	0
15	Guru Jambheshwar University of Science and Technology DHARMENDER SHARMA 9466170501	<u>25</u>	0	<u>25</u>	<u>25</u>	0	<u>25</u>	<u>25</u>	0	25	4	21
16	Gurugram Metropolitan Development Authority (GMDA) Sh. Abhinav Verma 9988030939	<u>266</u>	4	<u>262</u>	270	23	247	<u>244</u>	13	231	<u>47</u>	184
17	Gurugram University, Gurugram Sh. Akshay Sharma, JE 8197632737	<u>45</u>	0	45	<u>45</u>	1	<u>44</u>	<u>44</u>	7	37	<u>37</u>	0
18	Haryana Irrigation Research and Management Institute Sh. Digvijay Sharma 8053519393	7	1	<u>6</u>	<u>6</u>	1	<u>5</u>	<u>5</u>	0	<u>5</u>	2	3
19	Haryana Police Housing Corporation Limited Sh. Dhiraj Gupta, EE 9417317730	<u>631</u>	80	551	553	82	<u>471</u>	<u>469</u>	<u>45</u>	424	<u>103</u>	321
20	Haryana Power Generation Corporation Limited Ms. Yashna 9915436918	<u>434</u>	4	430	436	44	<u>392</u>	<u>386</u>	<u>11</u>	<u>375</u>	<u>213</u>	<u>162</u>
21	Haryana Renewable Energy Development Agency (HAREDA) Sh. Ajit Kumar Bhadu,	0	0	0	0	0	0	0	0	0	0	0

	9872955129											
22	Haryana Rural Development Fund Administration Board (HRDFA) Sh. Vishal Kharb 9041968104	0	0	0	0	0	0	0	0	0	0	0
23	Haryana School Shiksha Pariyojna Parishad GAURAV BARGUJAR 9466177323	<u>561</u>	20	<u>541</u>	<u>26</u>	<u>26</u>	0	0	0	0	0	0
24	Haryana Shehri Vikas Pradhikaran Sh. Amit Rathi, EE 9711880411	823	137	686	1183	480	703	683	20	663	183	480
25	Haryana State Agriculture Marketing Board Panchkula Sh. Ashish Gupta, SE 9466047318	<u>1605</u>	33	<u>1572</u>	<u>1598</u>	20	<u>1578</u>	<u>1535</u>	9	<u>1526</u>	93	1433
26	Haryana State Cooperative Labour& Construction Federation Limited Sh. Aman Dhiman 9468002209	1	0	1	1	0	1	1	0	1	1	0
27	Haryana State Cooperative Supply & Marketing Federation Limited (HAFED) Sh. Amit Dua, EE 9354224051	22	1	21	21	4	<u>17</u>	14	0	14	<u>6</u>	8
28	Haryana State Roads and Bridges Development Corporation Ms. Jyoti Sharma, Programmer 9646332165	<u>30</u>	14	16	<u>16</u>	1	<u>15</u>	<u>15</u>	1	14	<u>14</u>	0
29	Haryana State Warehousing Corporation Naresh Kumar 9873066066	103	0	103	103	0	103	103	0	103	<u>79</u>	24
30	Haryana Tourism Corporation	<u>21</u>	3	18	18	0	18	18	0	18	3	<u>15</u>
31	Haryana Vidyut Prasaran Nigam Limited Sh. Anant Sangwan, SE 9212520009	<u>1445</u>	132	1313	2352	1232	1120	1020	81	939	303	<u>636</u>
32 8 0	Horticulture Ms. Anita Sharma,	0	0	0	0	0	0	0	0	0	0	0

	Budget Officer 9463323820											
33	Housing Board Haryana Sh. Lalit, EE 7404316825	<u>21</u>	2	<u>19</u>	<u>19</u>	<u>6</u>	<u>13</u>	<u>13</u>	<u>2</u>	<u>11</u>	<u>2</u>	9
34	HSIIDC Sh. Anoop , EE 8558829224	1027	<u>19</u>	1008	1048	<u>67</u>	981	957	<u>38</u>	919	<u>235</u>	<u>684</u>
35	Indira Gandhi University Meerpur, Rewari Sh. Surinder Singh 9729540309	0	0	0	0	0	0	0	0	0	0	0
36	Irrigation & Water Resources Department Sh. Raveesh Pratap, EE 7696953947	<u>2534</u>	<u>81</u>	2453	<u>2497</u>	<u>38</u>	2459	2432	10	2422	380	2042
37	Kurukshetra University, Kurukshetra Sh. Pankaj Sharma 9464410848	<u>3</u>	1	2	<u>2</u>	0	2	<u>2</u>	0	2	<u>1</u>	1
38	Lala Lajpat Rai University (LUVAS), Hisar Er. Ravinder Kumar 9816502144	0	0	0	0	0	0	0	0	0	0	0
39	Maharana Pratap Horticultural University, Karnal Sh. Surender Singh, SDE 9053041475	7	0	7	7	1	<u>6</u>	<u>6</u>	<u>4</u>	2	2	0
40	Maharashi Dayanand University, Rohtak Sh. Jagdish Singh Dahiya 9991366698	<u>153</u>	0	153	<u>153</u>	<u>3</u>	<u>150</u>	<u>150</u>	<u>1</u>	149	<u>149</u>	0
41	MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant Design Engineer) 8568829007	1275	<u>172</u>	1103	<u>1102</u>	<u>40</u>	<u>1062</u>	<u>1015</u>	<u>61</u>	<u>954</u>	<u>262</u>	692
42	Municipal Corporation/Urban Local Bodies Sh. Gaurav Anand, EE 9779249515	23470	<u>679</u>	22791	<u>22819</u>	<u>484</u>	22335	22307	<u>609</u>	21698	<u>4649</u>	17049
43	Panchkula Metropolitan Development Authority Sh. Arvind Kumar, EE 9468434344	<u>50</u>	0	<u>50</u>	<u>53</u>	2	<u>51</u>	<u>50</u>	0	<u>50</u>	<u>27</u>	23
44 1	Pandit Lakhmi Chand State University of Performing &	0	0	0	0	0	0	0	0	0	0	0

	Visual Arts, Rohtak Sh. Devender Rathee, Dy. Registrar 9466628298											
45	Public Health Engineering Department Sanket Sharma EE 9466744148	<u>5594</u>	<u>579</u>	<u>5015</u>	<u>5873</u>	1007	<u>4866</u>	<u>4542</u>	207	4335	<u>917</u>	3418
46	Public Works Department Sh. Harish Bhatia 8283803804	<u>6549</u>	436	6113	6123	200	5923	<u>3756</u>	77	<u>3679</u>	<u>2873</u>	806
47	Shri Mata Mansa Devi Shrine Board, Panchkula Sh. Rakesh Pahuja, SDE 9815336655	<u>6</u>	0	<u>6</u>	<u>6</u>	0	<u>6</u>	<u>6</u>	1	<u>5</u>	<u>5</u>	0
48	Shri Vishwarkarma Skill University Sh. Naresh Sandhu, JE 9729969911	<u>8</u>	0	8	8	0	8	<u>8</u>	2	<u>6</u>	<u>6</u>	0
49	Skill Development and Industrial Training Department Sh. Raj Kumar, AD 8968068091	0	0	0	0	0	0	0	0	0	0	0
50	Sonipat Metropolitan Development Authority Sh. Amit Kaushik 8607262407	0	0	0	0	0	0	0	0	0	0	0
51	Uttar Haryana Bijli Vitran Nigam Limited Sh. J.S Nara 9416950002	<u>495</u>	4	<u>491</u>	<u>489</u>	<u>2</u>	487	<u>486</u>	<u>75</u>	411	204	207
52	YMCA Technical University Sh. Anil Sharma, SDE 8860451489	<u>27</u>	0	<u>27</u>	<u>27</u>	0	<u>27</u>	<u>27</u>	0	<u>27</u>	<u>26</u>	1
	Total	81711	2748	78963	81055	4424	76631	70176	2324	67852	12784	55068

	Contractor Works Score Status							
Sr.	Department Name (Nodal	Total	Score	work	pending to	awared sco	ore	Progress
No.	Officer Name and Mobile	Works	Awarde	Total	<=15 days	16-30	>30	%
	No.)	posted by	d to	Total	<=15 days			verificatio
		Contracto	Works			days	days	n
		rs	by					''
			concern					
			ed					
			Enginee					
			r in					
1			Charge					
1	Chaudhary Bansi Lal							
	University, Bhiwani							
	Sh. Dinesh Kumar Madan,							
	Professor							
	8199932069	<u>1</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
2	Chaudhary Devi Lal							
	University, Sirsa							
	Sh. Rakesh Kumar, EE							
	9896323322	<u>5</u>	<u>5</u>	0	<u>0</u>	<u>0</u>	0	100%
3		_	_	_	_		_	23,0
	Director Urban Local Bodies							
	Sh. Gaurav Anand, EE							
		4.40	4.42			•		1000/
	9779249515	<u>142</u>	<u>142</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
4	Fisheries							
	Sh. Surinder Pal							
	9466620706	<u>1</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
5	Haryana Renewable Energy							
	Development Agency							
	(HAREDA)							
	Sh. Ajit Kumar Bhadu, Project							
	Officer							
	9872955129	1	<u>1</u>	<u>0</u>	<u>0</u>	<u>0</u>	0	100%
6		_		_	_	_	_	
	Haryana State Cooperative							
	Supply & Marketing							
	Federation Limited (HAFED)							
	Sh. Amit Dua, EE							
	9354224051	<u>13</u>	<u>13</u>	0	<u>o</u>	<u>0</u>	0	100%
7	Haryana State Roads and							
	Bridges Development							
	Corporation							
	Ms. Jyoti Sharma,							
	Programmer	4.4	4.4			0		40004
	9646332165	<u>11</u>	<u>11</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
8	Haryana Tourism Corporation							
	Limited							
	Nitin Modi (Executive							
	Engineer)							
	9255004162	<u>7</u>	7	0	0	0	0	100%
	J2JJ004102	<u>/</u>	<u></u>	<u>U</u>	<u>U</u>	<u>U</u>	<u>U</u>	100%

9	Housing Board Haryana							
	Sh. Lalit, EE							
	7404316825	<u>9</u>	<u>9</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
10	HSIIDC							
	Sh. Anoop , EE							
	8558829224	<u>102</u>	<u>102</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
11	Kurukshetra University,							
	Kurukshetra							
	Sh. Pankaj Sharma							
	9464410848	<u>8</u>	<u>8</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
12	Maharashi Dayanand							
	University, Rohtak							
	Sh. Jagdish Singh Dahiya							
	9991366698	<u>14</u>	<u>14</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
13	Sonipat Metropolitan							
	Development Authority							
	Sh. Amit Kaushik							
	8607262407	<u>1</u>	<u>1</u>	0	<u>0</u>	<u>0</u>	0	100%
14	Uttar Haryana Bijli Vitran	_						
	Nigam Limited Sh. J.S Nara							
	9416950002	<u>93</u>	93	0	0	0	0	100%
15		<u> </u>	<u> </u>		<u> </u>	<u> </u>		100/0
13	YMCA Technical University Sh. Anil Sharma, SDE							
	8860451489				_	0		1000/
16	8860451489	<u>8</u>	<u>8</u>	<u>0</u>	<u>0</u>	<u>0</u>	<u>0</u>	100%
10								
	Haryana State Agriculture							
	Marketing Board Panchkula							
	Sh. Ashish Gupta , SE							
	9466047318	<u>520</u>	<u>518</u>	<u>2</u>	<u>1</u>	0	<u>1</u>	99%
17	Haryana Vidyut Prasaran	<u>320</u>	310		=	<u> </u>		3370
	Nigam Limited							
	Sh. Anant Sangwan, SE							
	9212520009	<u>218</u>	<u>216</u>	2	<u>2</u>	<u>0</u>	0	99%
18		210	210	<u> </u>	<u> </u>	<u> </u>		33/0
10	Municipal Corporation/							
	Urban Local Bodies							
	Sh. Gaurav Anand, EE							
	9779249515	<u>3437</u>	3421	<u>16</u>	<u>0</u>	<u>0</u>	<u>16</u>	99%
19	Haryana Police Housing							
	Corporation Limited							
	Sh. Dhiraj Gupta , EE							
	9417317730	104	102	<u>2</u>	<u>1</u>	<u>o</u>	<u>1</u>	98%
20	7 1 1/31//30	104	102	<u> </u>	<u> </u>	<u>U</u>	<u>_</u>	90%
20	Haryana School Shiksha							
	Pariyojna Parishad							
	GAURAV BARGUJAR							
	9466177323	<u>88</u>	97	<u>1</u>	<u>0</u>	<u>0</u>	1	98%
	34UU1//323	00	<u>87</u>	<u>+</u>	<u>U</u>	<u>U</u>	<u>1</u>	36%

21 Haryana Shehri Vikas									
Sh. Amit Rathi, EE 9711880411	21	Haryana Shehri Vikas							
STATISBO411		Pradhikaran							
22		Sh. Amit Rathi, EE							
Sanket Sharma EE 946744148 1991 1963 28 8 2 18 98%		9711880411	<u>472</u>	<u>466</u>	<u>6</u>	<u>0</u>	<u>0</u>	<u>6</u>	98%
9466744148 1991 1963 28 8 2 18 98%	22	Public Health Engg. Dept.							
23 Public Works Dept. (B&R) Sh. Harish Bhatia 8283803804 1928 1890 38 10 1 27 98% 28 28 28 28 28 28 28		Sanket Sharma EE							
23		9466744148	<u>1991</u>	<u>1963</u>	<u>28</u>	<u>8</u>	<u>2</u>	18	98%
Sh. Harish Bhatia 8283803804 1928 1890 38 10 1 27 98% 27 2883803804 1928 1890 38 10 1 27 98% 27 28 28 28 29 29 27 20 20 20 27 20 20 20	23	Public Works Dept.(B&R)				_			
See See See See See See See See See Se									
24 IRRIGATION Sh. Raveesh Pratap, EE 7696953947 1432 1402 30 21 0 9 97%			1928	1890	38	10	1	27	98%
Sh. Raveesh Pratap, EE	24		1320	1000	<u>50</u>				3070
T696953947									
25 Gurugram Metropolitan Development Authority (GMDA) Sh. Abhinav Verma 9988030939 75 72 3 0 0 3 96%			1/22	1402	20	21	0	0	070/
Development Authority (GMDA) Sh. Abhinav Verma 9988030939 75 72 3 0 0 3 96%	25		1432	1402	<u>30</u>	<u>Z1</u>	<u>U</u>	<u> </u>	97%
CGMDA Sh. Abhinav Verma 9988030939 75 72 3 0 0 3 96%	25	_							
Sh. Abhinav Verma 9988030939 75 72 3 0 0 3 96%									
9988030939									
26		Sh. Abhinav Verma							
Haryana Power Generation Corporation Limited Ms. Yashna 9915436918 119 115 4 0 0 4 96%		9988030939	<u>75</u>	<u>72</u>	<u>3</u>	<u>0</u>	<u>0</u>	<u>3</u>	96%
Corporation Limited Ms. Yashna 9915436918 119 115 4 0 0 4 96%	26								
Ms. Yashna 9915436918 119 115 4 0 0 4 96%		Haryana Power Generation							
9915436918		Corporation Limited							
27 Agriculture and Farmer Welfare Department Dr. Devinder Sihag, JD 9416380656 22 21 1 0 0 1 95% 28 Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 9 94% 29 Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94% 30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE		Ms. Yashna							
27 Agriculture and Farmer Welfare Department Dr. Devinder Sihag, JD 9416380656 22 21 1 0 0 1 95% 28 Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 9 94% 29 Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94% 30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE		9915436918	119	115	4	0	0	4	96%
Welfare Department Dr. Devinder Sihag, JD 9416380656 22 21 1 0 0 1 95% 28 Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 94% 29 Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94% 30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE 49 38 11 0 0 11 77%	27				_	_	_	_	
Dr. Devinder Sihag, JD 9416380656 22 21 1 0 0 1 95% 28 Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 94% 29 Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94% 30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE 49 38 11 0 0 11 77%									
9416380656 22 21 1 0 0 1 95%									
28 Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313 29 Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 215 0 0 125 94% 30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE			22	21	1	0	0	1	0E0/
University, Hisar Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 94%	20		<u> </u>	<u>Z1</u>	<u>±</u>	<u>U</u>	<u>U</u>	<u> </u>	33/0
Sh. Dharambir Malik, EE 9416278313 18 17 1 1 0 0 94%	20								
9416278313									
29		Sh. Dharambir Malik, EE							
Development and Panchayat Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94%		9416278313	<u>18</u>	<u>17</u>	<u>1</u>	<u>1</u>	<u>0</u>	<u>0</u>	94%
Sh. Veenus Nathalia, EE 9356925623 2248 2123 125 0 0 125 94%	29								
9356925623 2248 2123 125 0 0 125 94%		Development and Panchayat							
9356925623 2248 2123 125 0 0 125 94%		Sh. Veenus Nathalia, EE							
30 MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE		9356925623	2248	2123	125	0	0	125	94%
MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE	30					_	_		
COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89%		MICRO IRRIGATION &							
DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 216 2193 223 0 0 223 89% 31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE									
HARYANA (CADA) Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89%									
Sudesh Kumar (Assistant 8568829007 216 193 23 0 0 23 89%									
S568829007 216 193 23 0 0 23 89%		· ,							
31 Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% Gurugram University, Gurugram Sh. Akshay Sharma, JE			216	102	22	0	0	22	000/
Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530 49 38 11 0 0 11 77% Gurugram University, Gurugram Sh. Akshay Sharma, JE	24		210	193	<u>23</u>	<u>U</u>	<u>U</u>	<u>23</u>	85%
Sh. Rajesh Ninaniya, EE 49 38 11 0 0 11 77% 32 Gurugram University, Gurugram Sh. Akshay Sharma, JE 50 60 11 10 11 77%	31								
9812452530									
32 Gurugram University, Gurugram Sh. Akshay Sharma, JE									
Gurugram Sh. Akshay Sharma, JE			<u>49</u>	<u>38</u>	<u>11</u>	<u>0</u>	<u>0</u>	<u>11</u>	77%
Sh. Akshay Sharma, JE	32	Gurugram University,							
8197632737 17 12 5 0 0 5 70%									
		8197632737	<u>17</u>	<u>12</u>	<u>5</u>	<u>0</u>	<u>0</u>	<u>5</u>	70%

33	Haryana State Warehousing							
	Corporation							
	Naresh Kumar							
	9873066066	<u>14</u>	<u>9</u>	<u>5</u>	<u>0</u>	<u>0</u>	<u>5</u>	64%
34								
	Haryana Irrigation Research							
	and Management Institute							
	Sh. Digvijay Sharma							
	8053519393	<u>2</u>	1	1	0	0	1	50%
35	Faridabad Metropolitan							30,0
	Development Authority							
	(FMDA)							
	Sh. Ankit Bhardwaj, EE							
	9990606765	5	2	3	0	0	3	40%
26		<u> 2</u>	<u>2</u>	<u> </u>	<u>U</u>	<u>0</u>	<u> </u>	40%
36	Deen Bandhu Chootu Ram							
	University of Science &							
	Technology, Murthal							
	Vijay Kumar							
	9416232747	3	1	2	0	0	<u>2</u>	33%
37	Guru Jambheshwar						_	
	University of Science and							
	Technology							
	DHARMENDER SHARMA							
	9466170501	6	2	4	0	0	4	33%
38	Forests	<u>u</u>	<u> </u>		<u> </u>	<u> </u>		33/0
36	Sh. Rajesh Rana, DFO(HQ)							
	9417401427	31	0	31	<u>0</u>	<u>0</u>	31	0%
20		<u>51</u>	<u>U</u>	<u>51</u>	<u>U</u>	<u>U</u>	<u>31</u>	070
39	Gurgoan Technology Park							
	Limited	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
40	Haryana building & other							
	construction workers welfare							
	board	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
41								
	Haryana Forest Development							
	Corporation Limited	<u>2</u>	<u>0</u>	<u>2</u>	<u>0</u>	<u>0</u>	<u>2</u>	0%
42	Haryana Institute Of Public							
	Administration	<u>2</u>	<u>0</u>	<u>2</u>	<u>0</u>	<u>0</u>	<u>2</u>	0%
43								
	Haryana State Cooperative							
	Development Federation							
	Limited (HARCOFED)	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
44	,			_	_		_	
	Haryana State Cooperative							
	Housing Federation Limited	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
45								
	Ms. Anita Sharma, Budget							
	Officer							
	9463323820	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%

46								
	Law and Legislative	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
47	Medical Education and							
	Research	<u>3</u>	<u>0</u>	<u>3</u>	<u>0</u>	<u>0</u>	<u>3</u>	0%
48	Pandit Bhagat Dayal Sharma							
	University of health Sciences,							
	Rohtak	<u>2</u>	<u>0</u>	<u>2</u>	<u>0</u>	<u>0</u>	<u>2</u>	0%
49	Sainik and ArdhSainik							
	Welfare Department	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
50	Skill Development and							
	Industrial Training							
	Department							
	Sh. Raj Kumar, AD	<u>4</u>	<u>0</u>	<u>4</u>	<u>0</u>	<u>0</u>	<u>4</u>	0%
51	Social Justice and							
	Empowerment	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
52	5	•		,	•		•	00/
	Sports and Youth Welfare	<u>2</u>	<u>0</u>	<u>2</u>	<u>0</u>	<u>0</u>	<u>2</u>	0%
53	Transport Comissioner							
	Haryana	<u>1</u>	<u>0</u>	<u>1</u>	<u>0</u>	<u>0</u>	<u>1</u>	0%
	Total	13455	13087	368	44	3	321	97%



जनस्वास्थ्य अभियांत्रिकी विभाग, हरियाणा PUBLIC HEALTH ENGINEERING DEPARTMENT, HARYANA



Bays No. 13-18, Sector-4, Panchkula-134112 Ph. 0172-2561672, Website: https://phedharyana.gov.in SNK Toll Free No. 1800-180-5678

From

The Engineer-in-Chief, Haryana, Public Health Engineering Department, Panchkula.

To

The Engineer-in-Chief, Haryana Public Works Department (B&R), Chandigarh.

Memo No. 44828

-PHE/HEWP

Dated: - 14 05 2024

Subject: -

Proceedings of the meeting held on 19.04.2024 at 03:30 PM under the Chairmanship of Engineer-in-Chief (Roads), PWD (B&R) regarding changes in Common Bid Document (CBD) in Main Committee Room, Nirman Sadan, Plot No.1, Sector-33/A, Chandigarh.

Please find enclosed herewith the Proceedings of the subject cited meeting held on 19/04/2024 under the Chairmanship of Engineer-in-Chief (Roads), PWD (B&R) regarding changes in Common Bid Document (CBD).

I have been directed to request you to take further necessary action in the matter.

DA/ As above

Project Engineer (HEWP) for Engineer-in-Chief

Proceedings of the meeting held on 19.04.2024 at 03:30 PM under the Chairmanship of Engineer-in-Chief (Roads), PWD (B&R) regarding changes in Common Bid Document (CBD) in Main Committee Room, Nirman Sadan, Plot No.1, Sector-33/A, Chandigarh.

The attendance sheet of the members who attended the meeting is enclosed as Annexure-I.

The following changes proposed to be made in Common Bid Document (CBD) were discussed in the meeting.

Sr. No.	Section/ Part/ Clause (Page No.) of CBD	Existing Description (changes proposed to be made have been highlighted)	Amended Clause
pared perel pared perel	documents set documents set. set. set. set. set. set. set. se	with the following interest; the dispersion of the Haryana the Haryana should uplood a should uplood a comments. 2. In Clause Education of the Education of the Clause in Clause in the Clause in th	Interested bidders who are not registered on Haryana Engineering Works Portal should upload the following documents at the time of bidding: a. Mandatory Documents i. Proof of Constitution - Partnership deed (in case of the partnership firm registration); or Certificate of Incorporation (in case of Private limited company, public limited company, Public sector undertaking, Limited Liability Partnership, registration); or Any proof substantiating constitution (in the case of society, trust, AOP, Government department, local authority, statutory body registration.) ii. PAN Card iii. GST Certificate iv. Undertaking of Non-Blacklisting – (Certificate that contractor has not been blacklisted previously) v. Proof of immovable properties/self-certification that doesn't have any property vi. Cancelled Cheque / Proof of bank account vii. Proof of Address viii. The applicant himself or his employee (at least one) should be a Diploma Holder Engineer (Civil/Electrical/Agri./Hort.) as applicable. Accordingly, self-declaration certificate of applicant and his employee along with copy of Diploma certificate is to be submitted. ix. In case for electrical works the applicant or the employee of the applicant should submit valid Wireman License from Chief Electrical Inspector, Haryana

Sr. No.	Section/ Part/ Clause (Page No.) of CBD	Existing Description (changes proposed to be made have bee highlighted)	OF STREET STREET, STREET STREET, STREE
tender	CBD LOSED AND ASSESSED ASSESSED AND ASSESSED ASSESSED AND ASSESSED ASSESSED AND ASSESSED ASSESS	attended the meeting is enclosed in the transfer of the common Bid Document (Common Bid Docum	b. Optional Documents i. TAN Number Document ii. MSME Registration Certificate (If Applicable) iii. Form 26AS for last three years (Provided by Income Tax Department) iv. LLCs (Limited Liability Company) to upload last audited balance sheet v. Change of constitution of agency vi. Litigation History (If any) vii. List of completed works if any viii. List of Abandoned works (if any) ix. Any Other relevant documents
	Dr	veniment, the time of bidde or any public	IX. Any Other relevant documents
erijesta	to a Mon-Block of Allers o	blacklated previous blackl	In case during examination it is found that any bidder for this category of works has not submitted above mandatory documents or has submitted false documents his bid shall be rejected. (In this Clause, proposed changes have been made by shifting the second paragraph of Clause 4 'Qualification of the Bidder (A)' - 'Interested bidders who are not registered' to Clause 3 'Eligible Bidders', below point 3.2 with the following changes (mentioned in bold letters): 1. In Clause 4 (A), second paragraph: Interested bidders who are not registered on the Haryana Engineering Works Portal should upload the following documents at the time of bidding:
emaloy ma libit ma libit hori) nacista works to milicate works to milicate	heque i Production de la	property vi. Cencelled C vi. Cencelled C vii. Preof of Aide viii. The applican (at least one) she Engineer (Civili applicable. Acci certificate of app elong with or py to be submitted applicant or the sibrit about submit	2. In Clause 4 (A), point a. Mandatory Documents, point 'viii. Similar works experience for the category of registration has been removed. 3. In Clause 4 (A), point a. Mandatory Documents, the phrase "of registration" has been removed from point ix. Thus, the revised point ix is: "In case for electrical works the applicant or the employee of the applicant should submit a valid Wireman License from Chief Electrical Inspector, Haryana." 4. In clause 4 (A), point b. Optional Documents a new point as 'vii. List of completed works, if any.' has ben added

Sr.	Section/	Existing Description (changes	Amended Clause
No.	Part/ Clause (Page No.) of CBD	proposed to be made have been highlighted)	
2	Section 1/ Part A General/ Clause 3 Eligible Bidders 3.4 (Page No. 9)	(This Clause was previously 3.3, and now it has been proposed as the new Clause 3.4, as mentioned in the existing description of Sr. No. 1.)	Bidders shall not be under a declaration of ineligibility for corrupt and fraudulent practices by the Central Government, the State Government or any public undertaking, autonomous body, authority by whatever name called under the Central or the State Government.
3		iii. GST Certificate iv. Undertaking of Non- Blacklisting – (Certificate that	For works put to tender upto Rs. 25.00 Lacs, contractor's id on Haryana Engineering Works Portal. (No technical evaluation shall be carried out for this category).

r. lo.	Section/ Part/ Clause (Page No.) of CBD	proposed to be made have been highlighted)	Amended Clause	
	is retinue ad Jo	viii. Similar works experience for		
	one launos a	the category of registration		
	Central Govern	ix. The applicant himself or his		
	ns to inem	employee (at least one) should be		
	Apod anomonal	a Diploma Holder Engineer		
		(Civil/Electrical/Agri./Hort.) as applicable. Accordingly, self-		
	tate Governmen	declaration certificate of applicant		
		and his employee along with copy	Louworks but	
	tor s at on	of Diploma certificate is to be	B ROBU LUCA	
	ortica Portal (No	submitted.	POLEODE INDO	
	to carried on	x. In case of registration for	bys lesinded	
		electrical works the applicant or	red for being	
		the employee of the applicant	hald palpastal	
		should submit valid Wireman	registered are	
		License from Chief Electrical	the following of	
		Inspector, Haryana	netistalige# To	
		. O tienal Decuments	Interested bid	
		b. Optional Documents i. TAN Number Document	registered str	
		ii. MSME Registration Certificate	fellowing docu	
		(If Applicable)	of bidding:	
		iii. Form 26AS for last three years		
		(Provided by Income Tax	3, Mandatory	
		Department)	10 10015	
		iv LLCs (Limited Liability		
		Company) to upload last audited	to eteniline	
		halance sheet		
		v. Change of constitution of	national adduct	
		agency	sector under	
		vi. Litigation History (If any)	Linbilly Partn	
		vii. List of Abandoned works (i	or Any pro	
		any) viii Any Other relevan	tonstitution	
		viii. Any Other relevant documents	Society, trust,	
		documents (soot as	Inemhisqueb	
		In case during examination it is	s bod victulate	
		found that any bidder for thi	S	
		category of works has no	ot	
		submitted above mandator	У	
		documents or has submitte	4	
		false documents his bid sha	vetic betablished	
		be rejected.	ton Proof	
		ertification that		
A		vhegord v		
		. No long L auron	y Indianna 7 liv	

Sr. No.	Section/ Part/ Clause (Page No.) of CBD	Existing Description (changes proposed to be made have been highlighted)	Amended Clause
4	Section 1/ Part A General/ Clause 4 Qualification of the Bidder (B) (Page No. 10)	For works put to tender from Rs. 25.01 Lacs to Rs. 64.00 Lacs, a valid registration and contractor's id on Haryana Engineering Works Portal with proof of ownership/ lease of specified machinery/ manpower as listed in Clause 39 of this document. (Technical Evaluation shall be carried out as per the requirement specified in Clause 39 of this document and financial bid of only responsive qualifying bidders shall be opened)	For works put to tender from Rs. 25.01 Lacs to Rs. 64.00 Lacs, a valid enlistment certificate with proof of ownership/ lease of specified machinery/ manpower as listed in Clause 39 of this document and contractor's id on Haryana Engineering Works Portal. (Technical Evaluation shall be carried out as per the requirement specified in Clause 39 of this document and financial bid of only responsive qualifying bidders shall be opened)
5	Section 1/ Part F Award of Contract/ Clause 31 Award Criteria 31.1(ii) (Page No. 31)	To be within the available bid capacity adjusted to account for his bid price which is evaluated the lowest in any of the packages opened earlier than the one under consideration. In no case, the contract shall be awarded to any bidder whose available bid capacity is less than the evaluated bid.	To be within the available bid capacity adjusted to account for his bid price which is evaluated the lowest in any of the packages opened earlier than the one under consideration. In no case, the contract shall be awarded to any bidder whose available bid capacity is less than the evaluated bid for tender cost more than Rs. 64.00 Lacs.
6	Section 2/ Qualification Information / Clause 1.3.1 (Page No. 37)	Work performed as prime Contractor (in the same name and style) on construction works of a similar nature and volume over the last Five years.	(in the same name and style) on
7	Section 4-B/ Technical Condition for El Work /Point no. 20 (Page No. 119)	Only HYLAM make ISI make (I.S.2036-1995) white Bakelite sheet will be used without any extra cost.	Only ISI make (I.S.2036-1995) white Bakelite sheet will be used without any extra cost.

Sr. No.	Section/ Part/ Clause (Page No.) of CBD	Existing Description (changes proposed to be made have been highlighted)	Amended Clause
8	Section 4-B/ Additional Conditions for Mtc. Contract /Point no. 7 (Page No. 138)	The firm will deploy only trained and appropriate skilled personnel to keep the equipment properly adjusted and they will use all reasonable care to maintain the elevator in proper and safe operating conditions, which will include manpower i.e. 2 operators cum technician with 10 hr. shift of each on all the seven days of week.	(To be deleted) A had
	Section 7/ (I) Integrity Pact Format (Page No. 323)	(To be executed on plain paper and submitted alongwith Technical Bid/Tender documents for tenders having a value of Rs 1 cr. or above. To be signed by the bidder and same signatory competent/ authorized to sign the relevant contract on behalf of the State) This integrity Pact is made at on this day of 2021.	(To be executed on plain paper for tenders having a value of Rs 64.00 Lacs or above. To be signed by the successful bidder and same signatory competent/ authorized to sign the relevant contract on behalf of the State after issue of Notice to Proceed with the Work). This integrity Pact is made at on this day of ().

The meeting ended with a vote of thanks to the chair.

Annexure-I

List of Attendees who were attending the meeting.

Sr. No.	Name of Officer	Designation	Name of Department
1	Sh. Rajeev Yadav	EIC (Roads)	PWD (B&R)
2	Sh. Asheim Khanna	EIC	PHED
3	Sh. Rakesh Chauhan	EIC	I&WRD
4	Sh. Rajiv Batish	CE (Mech.)	PHED
5	Sh. Rajesh Ahuja	CE Elect.	PWD (B&R)
6	Sh. Kuldeep Rana	CE (NCR)	PWD (B&R)
7	Sh. Arun Jagga	CE(Buildings)	PWD (B&R)
8	Sh. Sunil Kundu	CE (Bridges)	PWD (B&R)
9	Sh. N.K. Tomar	CE (Roads)	PWD (B&R)
10	Sh. V.S. Malik	CE (NH)	PWD (B&R)
11	Sh. Arun Kumar	CE (Mech.)	PWD (B&R)
12	Sh. Sandeep Bishnoi	CE	I&WRD
13	Sh. Vishal Kumar	SE (Buildings)	PWD (B&R)
14	Sh. Anoop Kumar	AGM (Engg.)	HSIIDC
15	Sh. Harish Bhatia	SEO	PWD (B&R)
16	Sh. Dhiraj Kumar Gupta	EE(V&Q)	HPHC



जनस्वास्थ्य अभियांत्रिकी विभाग, हरियाणा PUBLIC HEALTH ENGINEERING DEPARTMENT, HARYANA

Annexure-G

Bays No. 13-18, Sector-4, Panchkula-134112 Ph. 0172-2561672, Website: https://phedharyana.gov.in SNK Toll Free No. 1800-180-5678

From

The Engineer-in-Chief, Haryana,
Public Health Engineering Department,

Panchkula.

To

The Engineer-in-Chief, Haryana Public Works Department (B&R), Chandigarh.

Memo No.83414

-PHE/HEWP

Dated: - 26 |09 | 2024

Subject: -

Proceedings of the meeting held on 19.04.2024 at 03:30 PM under the Chairmanship of Engineer-in-Chief (Roads), PWD (B&R) regarding changes in Common Bid Document (CBD) in Main Committee Room, Nirman Sadan, Plot No.1, Sector-33/A, Chandigarh.

nuigann

Kindly refer this office Memo No. 44828-PHE/HEWP dated 14/05/2024 vide which Proceedings of the subject cited meeting held on 19/04/2024 under the Chairmanship of Engineer-in-Chief (Roads), PWD (B&R) regarding changes in Common Bid Document (CBD) were sent to your office with request to take further necessary action in the matter. The action in the matter is awaited from your office.

I have been directed to request you to expedite the necessary action regarding the proposed changes in the Common Bid Document (CBD) as per the Proceedings of subject cited meeting.

Project Engineer (HEWP for Engineer-in-Chief

New Proposed Changes to be Added to the Common Bid Document (CBD):

The following new clauses are proposed to address gaps in the CBD regarding the death of a contractor and the death of a partner or director in a firm/company:

1. Termination of Contract on Death of Contractor (Proprietorship Firm):

Currently, the **Common Bid Document (CBD)** does not include any provision regarding the termination of a contract in the event of the contractor's death. To address this gap, it is proposed to add a new clause referring to **Clause 35 of the CPWD Code**, which states:

"Without prejudice to any of the rights or remedies under this contract, if the contractor dies, the Engineer-in-Charge on behalf of the President of India shall have the option of terminating the contract without levy of compensation to the contractor."

Proposed Clause for CBD:

"Without prejudice to any of the rights or remedies under this contract, if the contractor dies, the Engineer-in-Charge on behalf of the shall have the option of terminating the contract without levy of compensation to the contractor."

This amendment will ensure uniformity and provide a clear framework for addressing such situations.

2. Provisions for Death of Partner/Director:

The **Common Bid Document (CBD)** currently does not include any provision regarding the changes required in the constitution of a firm or company in the event of the death of a partner or director. To address this gap, it is proposed to add a new clause referring to **Clause 9.7 of the CPWD Code**, which states:

"In case of death of any partner/director, surviving partners/directors shall fill up Annexure-VI afresh online in CEMS portal for removal of the deceased partner/director from the constitution of the firm/company preferably within three months of the death of the partner/director. The death certificate of the deceased partner/director shall be uploaded on CEMS portal."

In case of death, prior approval is not applicable. The enlistment entity uploads the documents on the CEMS portal for acknowledgment from bank, Income Tax, and GST authorities for required changes in constitution after the death of a partner/director. Member Secretary of the Advisory Committee shall issue a change of constitution order within one month of receipt of the application by the surviving partner(s)/director(s). If the information provided is found to be wrong, forged, or illegal, criminal proceedings shall be initiated by the Enlisting Authority after providing an opportunity to the surviving partner(s)/director(s) to explain the discrepancy."

Proposed Clause for CBD:

"In case of death of any partner/director, surviving partners/directors shall apply for removal of the deceased partner/director from the constitution of the firm/company preferably within three months of the death. The death certificate of the deceased partner/director shall be submitted."

Further, surviving partner(s)/director(s) shall submit the necessary documents for acknowledgment from banks, Income Tax, and GST authorities, etc., to make the required changes in the constitution after the death of a partner/director. The concerned competent authority shall issue the change of constitution order within one month of receiving the application from the surviving partner(s)/director(s).

If the information provided is found to be incorrect, forged, or illegal, criminal proceedings shall be initiated by the concerned authority after giving the surviving partner(s)/director(s)/society president an opportunity to explain the discrepancy.

Select Functional Roles

Executive Engineer

Contractors Registration

Estimate Template Master

Work Allotment Management System +

Dashboard

e-Estimate

e-DNIT

NS Master

E-Billing

Activity

HSR Master

Help and Support

Rate Contract

Agenda of Estimate

Report

Annexure-

Hello, Dummy EE

Dashboard for Project Packages



Administrative Approval
15-09-2023

Technical Sanction Date
15-11-2023

Gurugram

Sohna

Town/Village Sohna GPS Coordinate [Coordinate] Scope of Work Construction of Sewage Treatment Plant, power house and laying of pipeline along with connection of Electrical Equipements

Project Name: STP GRG & Pipeline Laying Sohna

Project Cost (in Lacs)
250.00

Expenditure (in Lacs)
50.00

Total No. of Packages
4

Project Start Date

Project End Date 28-11-2025


01-01-2024


Project Completion Status







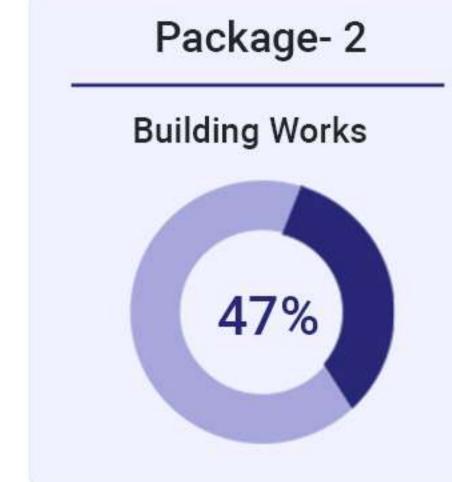

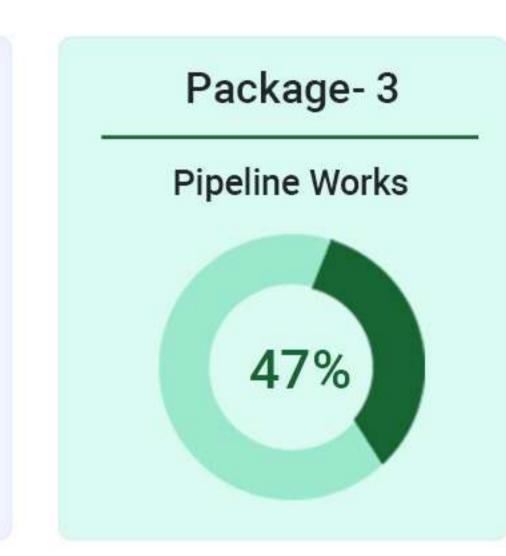



Description	Target Date	Actual Date
DNIT		
Allotment		
Start		

Description	Target Date	Actual Date
DNIT		
Allotment		
Start		

Description	Target Date	Actual Date
DNIT		
Allotment		
Start		

Description	Target Date	Actual Date
DNIT		
Allotment		
Start		

Key Project Staff

Name	Designation	Office Address
Sh. Ramesh Kumar	Junior Engineer	PHED, SDE Office, Sohna
Sh. Vikas Singh	Sub-Divisional Engineer	PHED, SDE Office, Sohna
Sh. SK Bhardwaj	Executive Engineer	PHED, Division No. 1, Gurgaon

Permissions from Other Departments

S. No.	Description of Permission Required	Department	Date of Application for Permission	Date of Receipt of Permission
1	Consent to Operate	State Pollution Control Board	12-10-2023	28-10-2023
2	STP CTE	National Green Tribunal	15-10-2023	04-11-2023
3	Environmental Clearance	National Green Tribunal	24-10-2023	11-12-2023
4	Pollution Clearance	State Pollution Control Board	07-11-2023	12-12-2023
5	Master Plan	Municipality	04-10-2023	10-10-2023
6	STP CTO	National Green Tribunal	180	520

Select Functional Roles

Executive Engineer

Contractors Registration

Estimate Template Master

Work Allotment Management System +

Dashboard

e-Estimate

e-DNIT

NS Master

E-Billing

Activity

HSR Master

Help and Support

Rate Contract

Agenda of Estimate


Report

+

+

Annexure-J

Dashboard for Contract Agreement

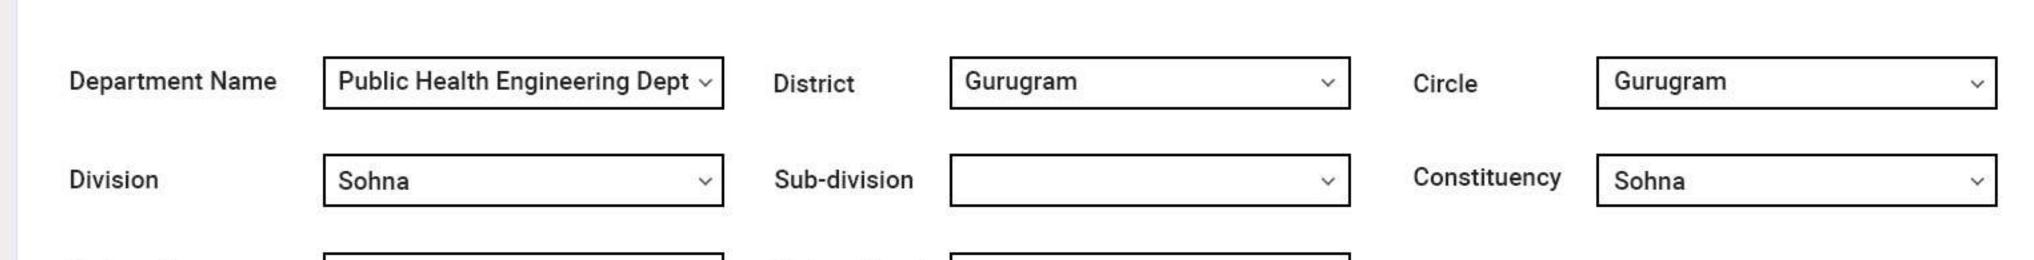

STP GRG Sohna 6 MLD

Jal Jeevan Mission

Contract Date
01-Jan-24

Project Name

Contract Finish
31-Dec-24

STP GRG Sohna 6 MLD

Forecast Finish
15-Feb-25

Budget Head

Delay/Ahead (Days)
- 44
















Key Performance Index

Total Cost	₹ 1,00,00,000.00	Remaining Cost
Remaining Cost 🕕	₹ 33,00,000.00	 Expenditure Cost
Expenditure Incurred	₹ 50,00,000.00	
Schedule Variance 🕕	₹ 15,0000.00	
Shedule Performance Index (SPI) 🕕	0.89	
Cost Performance Index (CPI) (i)	1.00	


Milestones

	Milestone to be Achieves (Physcial % Completion)	Target Date	Milestone Achievement Date
Milestone 1	20%	13-03-2024	24-03-2024
Milestone 2	50%	02-07-2024	20-07-2024
Milestone 3	75%	01-10-2024	
Milestone 4	100%	31-12-2024	

Planned vs Actual % (Activity Wise)

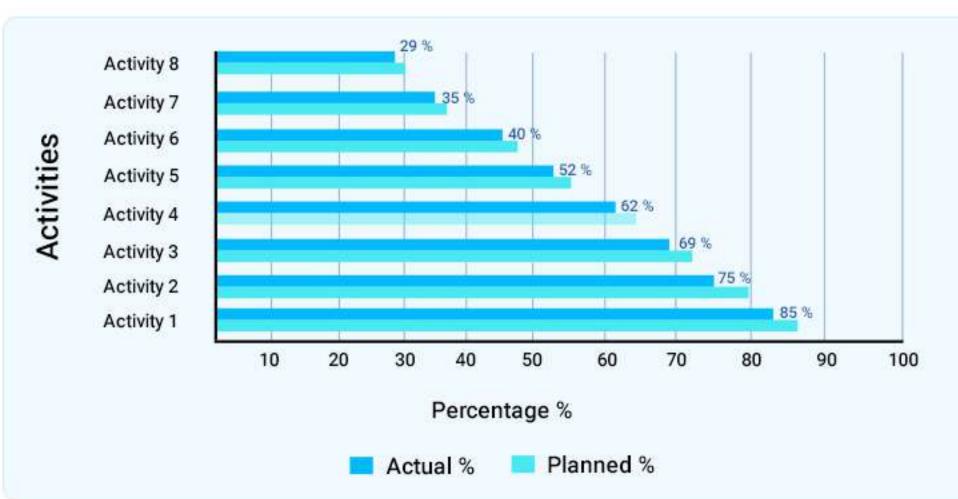

Project Timeline Graph

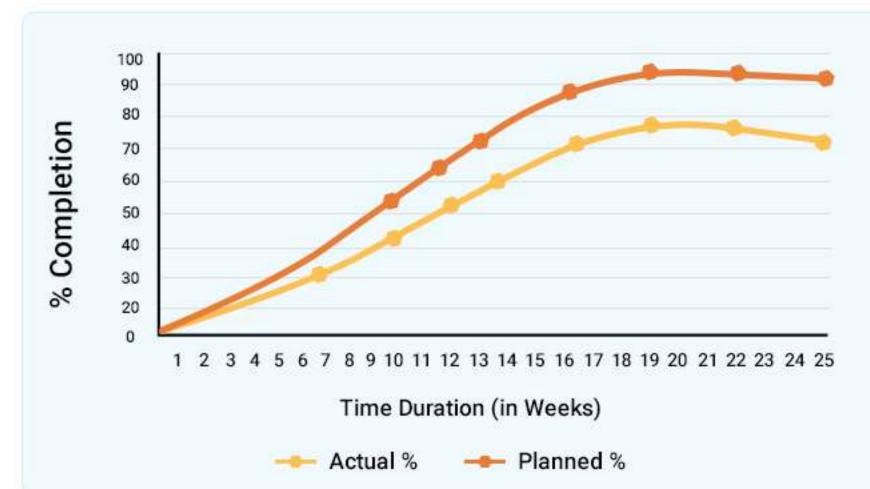

*Note - Following tect to come in (i) (i button) :

1. Schedule variance measures the difference between the planned project timeline and the actual progress achieved.

SV = EV-PV

EV (Earned Value is the value of work actually performed),

PV (Planned Value is the value of work that was planned to be performed by a specific time)

2. The Schedule Performance Index (SPI) is a measure of schedule efficiency.

SPI = EV/PV

If, SPI>1, Project is Ahead of Schedule

SPI=1, Project is On Schedule

SPI<1, Project is Behind Schedule

3.The Cost Performance Index (CPI) is a measure of cost efficiency.

CPI = EV/AC

If,CPI>1, Project is Under Budget

CPI=1, Project is on Budget

CPI<1, Project is Over Budget

4. Remaining Cost of the work yet to be executed

Annexure-K

	Donautmant	Entries of Capital Works in specific Modules						
Sr. No.	Department Nodal Officer Contact No.	e- Estimate	DNIT	e- Tendering	Allotment of Work	e-MB & Billing	Payments	
	Total	82314	70862	68322	56115	53176	4063	
1	Agriculture and Farmer Welfare Department Dr. Devinder Sihag, JD 9416380656	110	99	96	76	95	0	
2	Bhagat Phool Singh Mahila Vishwavidyalaya, Khanpur Kalan, Sonepat	0	0	0	0	0	0	
3	Chaudhary Bansi Lal University, Bhiwani Sh. Dinesh Kumar Madan, Professor 8199932069	8	8	8	3	1	0	
4	Chaudhary Charan Singh Haryana Agricultural University, Hisar Sh. Dharambir Malik, EE 9416278313	61	28	27	10	0	0	
5	Chaudhary Devi Lal University, Sirsa Sh. Rakesh Kumar, EE 9896323322	0	0	0	0	0	0	
6	Chaudhary Ranbir Singh University, Jind Sh. Jasvir Singh, Associate Professor 9466778222	9	9	7	4	0	0	
7	Dakshin Haryana Bijli Vitran Nigam Limited Sh. Rajesh Ninaniya, EE 9812452530	410	340	327	58	56	0	
8	Deen Bandhu Chootu Ram University of Science & Technology, Murthal Vijay Kumar 9416232747	15	1	0	0	0	0	
9	Development and Panchayat Sh. Veenus Nathalia, EE 9356925623	33918	29333	28250	26911	16034	0	
10	FARIDABAD CITY TRANSPORT SERVICES LIMITED Sh. Arbind Kumar 8510005801	0	0	0	0	0	0	
11	Faridabad Metropolitan Development Authority (FMDA) Sh. Ankit Bhardwaj, EE 9990606765	192	165	160	118	233	0	
12	Faridabad Smart City Sh. Gyan Prakash Wadhwa, DGM(Engg) 9711876119	11	10	9	0	0	0	
13	Fisheries Sh. Surinder Pal 9466620706	0	0	0	0	0	0	
14	Forests Sh. Rajesh Rana, DFO(HQ) 9417401427	0	0	0	0	0	0	
15	Guru Jambheshwar University of Science and Technology DHARMENDER SHARMA 9466170501	25	14	14	12	0	0	

16	Gurugram Metropolitan Development Authority (GMDA) Sh. Abhinav Verma 9988030939	275	253	239	189	290	0
17	Gurugram University, Gurugram Sh. Akshay Sharma, JE 8197632737	47	46	38	0	0	0
18	Haryana Irrigation Research and Management Institute Sh. Digvijay Sharma 8053519393	7	5	5	3	0	0
19	Haryana Police Housing Corporation Limited Sh. Dhiraj Gupta, EE 9417317730	641	323	291	214	9	0
20	Haryana Power Generation Corporation Limited Ms. Yashna 9915436918	444	391	382	166	202	0
21	Haryana Renewable Energy Development Agency (HAREDA) Sh. Ajit Kumar Bhadu, Project Officer 9872955129	0	0	0	0	0	0
22	Haryana Rural Development Fund Administration Board (HRDFA) Sh. Vishal Kharb 9041968104	0	0	0	0	0	0
23	Haryana School Shiksha Pariyojna Parishad GAURAV BARGUJAR 9466177323	587	457	412	247	404	0
24	Haryana Shehri Vikas Pradhikaran Sh. Amit Rathi, EE 9711880411	844	690	663	487	3174	0
25	Haryana State Agriculture Marketing Board Panchkula Sh. Ashish Gupta, SE 9466047318	1610	1540	1527	1446	6853	2667
26	Haryana State Cooperative Labour& Construction Federation Limited Sh. Aman Dhiman 9468002209	1	1	1	0	0	0
27	Haryana State Cooperative Supply & Marketing Federation Limited (HAFED) Sh. Amit Dua, EE 9354224051	22	14	14	8	5	0
28	Haryana State Roads and Bridges Development Corporation Ms. Jyoti Sharma, Programmer 9646332165	30	16	15	0	0	0
29	Haryana State Warehousing Corporation Naresh Kumar 9873066066	105	105	105	28	7	0
30	Haryana Tourism Corporation Limited Nitin Modi (Executive Engineer) 9255004162	21	18	18	15	0	0
31 52	Haryana Vidyut Prasaran Nigam Limited Sh. Anant Sangwan, SE 9212520009	1475	1051	964	654	507	0

32	Horticulture Ms. Anita Sharma, Budget Officer 9463323820	0	0	0	0	0	0
33	Housing Board Haryana Sh. Lalit, EE 7404316825	21	14	11	9	17	0
34	HSIIDC Sh. Anoop , EE 8558829224	1041	967	946	690	527	0
35	Indira Gandhi University Meerpur, Rewari Sh. Surinder Singh 9729540309	0	0	0	0	0	0
36	Irrigation & Water Resources Department Sh. Raveesh Pratap, EE 7696953947	2542	2448	2421	2063	5625	0
37	Kurukshetra University, Kurukshetra Sh. Pankaj Sharma 9464410848	3	2	2	1	0	0
38	Lala Lajpat Rai University (LUVAS), Hisar Er. Ravinder Kumar 9816502144	0	0	0	0	0	0
39	Maharana Pratap Horticultural University, Karnal Sh. Surender Singh, SDE 9053041475	8	6	3	0	0	0
40	Maharashi Dayanand University, Rohtak Sh. Jagdish Singh Dahiya 9991366698	157	152	151	0	0	0
41	MICRO IRRIGATION & COMMAND AREA DEVELOPMENT AUTHORITY HARYANA (CADA) Sudesh Kumar (Assistant Design Engineer) 8568829007	1273	1024	969	698	1079	0
42	Municipal Corporation/Urban Local Bodies Sh. Gaurav Anand, EE 9779249515	23599	22468	21796	17413	12959	0
43	Panchkula Metropolitan Development Authority Sh. Arvind Kumar, EE 9468434344	52	50	50	23	18	0
44	Pandit Lakhmi Chand State University of Performing & Visual Arts, Rohtak Sh. Devender Rathee, Dy. Registrar 9466628298	0	0	0	0	0	0
45	Public Health Engineering Department Sanket Sharma EE 9466744148	5606	4575	4323	3538	4820	1396
46	Public Works Department Sh. Harish Bhatia 8283803804	6607	3709	3627	812	154	0
47	Shri Mata Mansa Devi Shrine Board, Panchkula Sh. Rakesh Pahuja, SDE 9815336655	6	6	5	0	0	0
48	Shri Vishwarkarma Skill University Sh. Naresh Sandhu, JE 9729969911	8	8	6	0	0	0

49	Skill Development and Industrial Training Department Sh. Raj Kumar, AD 8968068091	0	0	0	0	0	0
50	Sonipat Metropolitan Development Authority Sh. Amit Kaushik 8607262407	0	0	0	0	0	0
51	Uttar Haryana Bijli Vitran Nigam Limited Sh. J.S Nara 9416950002	496	489	413	218	107	0
52	YMCA Technical University Sh. Anil Sharma, SDE 8860451489	27	27	27	1	0	0
	Total	82314	70862	68322	56115	53176	4063



HARYANA ENGINEERING WORKS PORTAL PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



From

The Project Director,
Haryana Engineering Works Portal (HEWP),
-cum-Chief Engineer (Rural),
O/o Engineer-in-Chief, Haryana,
Public Health Engineering Department,
Panchkula.

To

- The Engineer-in-Chief,
 Haryana PW (B&R) Department
- The Engineer-in-Chief, Haryana Public Health Engineering Department
- The Engineer-in-Chief, Haryana Irrigation & Water Resources Department
- 4. The Engineer-in-Chief, Haryana State Agriculture Marketing Board Panchkula
- The Chief Engineer, Development and Panchayat Department, Haryana
- 6. The Chief Engineer, Urban Local Bodies Department, Haryana
- The Chief Engineer, Haryana State Industrial and Infrastructure Development Corporation
- The Chief Engineer, Faridabad Metropolitan Development Authority
- The Chief Engineer, Gurugram Metropolitan Development Authority
- The Chief Engineer, Haryana Police Housing Corporation Limited
- 11. The Chief Engineer, Housing Board, Haryana



HARYANA ENGINEERING WORKS PORTAL PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hrv.gov.in



- 12. The Chief Engineer, Haryana Shehri Vikas Pradhikaran
- 13. The Chief Engineer (PD & C), Haryana Vidyut Prasaran Nigam Limited
- 14. The Chief Engineer (PD & C), Uttar Haryana Bijli Vitran Nigam Limited
- 15. The Chief Engineer (PD & C),
 Dakshin Haryana Bijli Vitran Nigam Limited
- 16. The Chief Engineer (Admin.),
 Haryana Power Generation Corporation Limited
- 17. The Chief Engineer,
 Micro Irrigation & Command Area Development Authority, Haryana
- 18. The Principal Director,
 Haryana Irrigation Research and Management Institute
- The Managing Director,
 Haryana State Roads and Bridges Development Corporation
- 20. The Executive Engineer, Haryana School Shiksha Pariyojna Parishad

Memo No. 15528 - 15582

/HEWP

Dated: 17/02/2025

Subject:

Proceedings of 2nd meeting of the Steering Committee of Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP held on 28.01.2025 under the Chairmanship of Commissioner & Secretary to Govt. Haryana PHE Department.

Please find enclosed herewith the Proceedings of 2nd meeting of the Steering Committee of the Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP, held on 28.01.2025 under the Chairmanship of Commissioner & Secretary to Govt. Haryana PHE Department, for information and necessary action.

DA / Proceedings of meeting

Project Engineer HEWP for Project Director HEWP



HARYANA ENGINEERING WORKS PORTAL PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Endst. No. 15528- 15582

/HEWP

Dated: 17/02/2525

A copy of above is forwarded to the Director General, Supplies & Disposals, Haryana for information and necessary action with reference to Item No. 2/2 (b) of the Proceedings.

DA/ Proceedings of meeting

Project Engineer HEWP for Project Director HEWP

Endst. No. 15528-15582

/HEWP

Dated: 17/02/2025

A copy of above is forwarded to the Departments/ Boards/ Corporations/ Universities etc. (list attached at Annexure 'A') for information and necessary action.

DA/ Proceedings of meeting

Project Engineer HEWP for Project Director HEWP

Endst. No. 15528-15582

/HEWP

Dated: 17/02/2625

A copy is forwarded to OSD to Commissioner & Secretary to Govt. Haryana Public Health Engineering Department for the kind information of the Officer please.

DA/ Proceedings of meeting

Project Engineer HEWP for Project Director HEWP



HARYANA ENGINEERING WORKS PORTAL PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



ANNEXURE-A

- The Managing Director, Agriculture and Farmers Welfare Department.
- 2. The Managing Director, Fisheries Department, Haryana.
- 3. The Managing Director, Forests Department, Haryana.
- 4. The Managing Director, Horticulture Department, Haryana.
- The Director General, Local Audit Department, Haryana.
- The Director, Skill Development & Industrial Training Department.
- The Director, Haryana State Cooperative Supply and Marketing Federation Limited.
- The Director General,
 The Haryana State Cooperative Labour & Construction Federation Limited.
- The Chief Executive Officer, Shri Mata Mansa Devi Shrine Board Panchkula, Haryana.
- The Managing Director, Haryana Rural Development Fund Administration Board, Chandigarh.
- The Managing Director, Haryana State Warehousing Corporation.
- The Managing Director, Haryana Tourism Corporation Limited.
- 13. The Chief Executive Officer,
 Sonipat Metropolitan Development Authority.
- The Chief Executive Officer, Panchkula Metropolitan Development Authority.
- The Director General, Haryana Renewable Energy Development Agency.
- The Chief Executive Officer, Faridabad Smart City Limited.



HARYANA ENGINEERING WORKS PORTAL PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112
Website: https://works.haryana.gov.in
Phone Number: 0172-2566393
Email: info-hewp.pwd@hry.gov.in



- The Chief Executive Officer, Faridabad City Transport Services Limited.
- 18. The Vice Chancellor, Bhagat Phool Singh Mahila Vishwavidyalaya, Khanpur Kalan, Sonepat.
- The Vice Chancellor, Chaudhary Bansi Lal University, Bhiwani.
- 20. The Vice Chancellor, Choudhary Charan Singh Haryana Agricultural University Hisar.
- 21. The Vice Chancellor, Chaudhary Devi Lal University, Sirsa.
- 22. The Vice Chancellor, Chaudhary Ranbir Singh University, Jind.
- 23. The Vice Chancellor,
 Dada Lakhmi Chand State University of Performing and Visual Arts, Rohtak.
- 24. The Vice Chancellor,
 Deen Bandhu Chootu Ram University of Science & Technology, Murthal
- 25. The Vice Chancellor, Gurugram University, Gurugram.
- 26. The Vice Chancellor, Guru Jambheshwar University of Science & Technology, Hisar.
- 27. The Vice Chancellor, Indira Gandhi University, Meerpur, Rewari.
- 28. The Vice Chancellor, J.C Bose University of Science and Technology, YMCA, Faridabad.
- The Vice Chancellor, Kurukshetra University, Kurukshetra.
- 30. The Vice Chancellor, Lala Lajpat Rai University of Veterinary & Animal Sciences (LUVAS), Hisar
- 31. The Vice Chancellor,
 Maharana Pratap Horticultural University, Karnal.
- 32. The Vice Chancellor, MD University, Rohtak.
- 33. The Vice Chancellor, Shri Vishwakarma Skill University, Haryana.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Proceedings of the 2nd Meeting of the Steering Committee of Project Management Unit (PMU) of Haryana Engineering Works Portal (HEWP) held on 28.01.2025 under the Chairmanship of Commissioner & Secretary to Govt. Haryana, PHE Department.

The 2nd Meeting of the Steering Committee of the Project Management Unit (PMU) of the Haryana Engineering Works Portal (HEWP) was held on 28.01.2025 at 11:00 AM under the Chairmanship of the Commissioner & Secretary to Govt. Haryana, Public Health Engineering Department at the Conference Hall of the Office of Engineer-in-Chief, Haryana PHE Department, Bay No. 19-20, Sector-4, Panchkula.

Participants

- The Attendance Sheet of members who participated physically is attached as **Annexure-I**.
- The list of members and participants who attended the meeting via Video Conferencing is attached as **Annexure-II**.

Project Director, HEWP, welcomed Commissioner & Secretary to Govt. Haryana, PHED and other members to the 2nd meeting of Steering Committee. At the outset, agenda of meeting and a brief presentation was placed before the Committee. The Project Director explained all the agenda points to the Committee as per agenda sequences.

Agenda-Wise Proceedings:

Item No. 2/1: Confirmation of the proceedings of the 1st meeting

It was informed to the members of Steering Committee that no observations have been received from any members for the 1st meeting of Steering Committee. Hence, proceedings of 1st meeting of Steering Committee was confirmed and approved.

Item No. 2/2: Action Taken Report on the decisions taken in the 1st meeting

The point wise action taken report on the decision taken in 1st meeting of Steering Committee was discussed in the meeting and following decisions were taken:



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



a) The Chairman desired that the file for the agenda for meeting of Apex Committee of PMU for HEWP be put up.

(Action: - HEWP Team)

b) It was informed to the Committee that in the 1st meeting of Steering Committee, the Chairman had asked the Director General, Supplies & Disposals, Haryana to take necessary action on the directions of Hon'ble CM Haryana regarding transfer of e-service fee collected per bid on the NIC e-Tendering Portal to the designated account of the HEWP. However, action in this matter is pending. The Chairman asked the Project Director HEWP to follow up with DG, Supplies & Disposals, Haryana.

(Action: - DG, Supplies & Disposals, Haryana)

c) It was informed to the Committee that API for BoQ comparative summary has not yet been provided by NIC. The Chief Engineer, ULB raised that price bid of the contractors may also be made fetched through API from NIC eTendering website after financial opening of a tender. The Chairman desired to convene the meeting with highest level of NIC Delhi officials to resolve this issue.

(Action: - NIC, HEWP Team)

d) The Project Director informed the Committee that several departments are still conducting offline tender allotments. The Chairman directed to stop the offline allotments and it was decided that in future all departments will adopt the online allotment for the works processed through HEWP.

(Action: - All Govt. Organizations on-boarded on HEWP)

e) The revision of HSR is under process with PWD (B&R). The EIC (Buildings)-cum-HoD, PWD (B&R) informed that a proposal would be submitted to the Government for establishing a dedicated PMU for the HSR revision on sustainable basis.

(Action: - PWD (B&R))

Item No. 2/3: Government organizations on-boarded on HEWP

This agenda item was presented for the information of Committee.

Item No. 2/4: Key statistics of HEWP

This agenda item was presented for the information of Committee.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Item No. 2/5: Department-wise progress of works on HEWP

The status of estimates Administratively Approved and Technically Sanctioned, DNITs approved, Tenders floated and Allotments made on HEWP was informed to the Committee. The Chairman observed that there is significant difference between numbers of tenders floated and tenders allotted by PWD (B&R). The EIC (Buildings)-cum-HoD, PWD (B&R), informed the Committee that all future allotments would be conducted through HEWP. It was decided that in future all departments will adopt the online allotment for the works processed through HEWP.

(Action: - All Govt. Organizations on-boarded on HEWP)

Item No. 2/6: Contractor works pending for scoring

This agenda item was presented for the information of Committee and it was decided that all departments will expedite the scoring of pending contractor works.

(Action: - All Govt. Organizations on-boarded on HEWP)

Item No. 2/7: Integration of Banks with HEWP

It was informed to the Committee that the Finance Department has authorized four banks (SBI, PNB, BOB and UBI) for integration with the HEW Portal to facilitate the payment of contractor bills. The Chief Engineer, ULB informed that various local bodies have accounts with multiple banks that need integration. However, the Finance Department has authorized only four banks, and they cannot proceed with integration with any single bank. The Chairman directed the Project Director, HEWP, to arrange a meeting between bank and ULB official to explore this matter.

(Action: - ULB Department, HEWP Team)

Item No. 2/8: Registration-cum-Enlistment Rules for Contractors

It was informed to the Committee that the draft **Registration-cum-Enlistment Rules for Contractors-2023** were prepared by PWD (B&R) and submitted to Govt. for approval. EIC (Buildings)-cum-HoD, PWD (B&R), confirmed that these rules have been approved by Govt. and matter is being followed up with the Government for issuing the notification.

(Action: - PWD (B&R))



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula - 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393

Email: info-hewp.pwd@hry.gov.in

Item No. 2/9: Proposed changes in Common Bid Document (CBD)

It was informed to the Committee that a letter proposing changes to the Common Bid Document (CBD) was submitted to PWD (B&R). The EIC (Buildings)-cum-HoD, PWD (B&R) informed that they have reviewed the proposed changes and assured further action to

incorporate the proposed changes in the CBD.

The new clauses proposed to be added to CBD regarding 'Termination of Contract on Death of Contractor (Proprietorship Firm)' and 'Provisions for Death of Partner/Director' were

discussed in the meeting.

The Chief Engineer, Development & Panchayat requested to make amendment in Clause 43

(Section-3, Part-I, D. Cost Control) of CBD and informed that reference for the same has

already been sent vide memo no. PRC/2025/186 dated 23.01.2025.

It was decided that a meeting shall be convened with PWD (B&R) to discuss addition of

these new clauses and amendment to CBD.

The Chief Engineer, ULB, raised concerns regarding the definition of "Construction works of similar nature" which needs to be defined in CBD. The Project Director suggested that "Construction works of similar nature" can be defined in ITB/Clause 39.1 for clarity by

concerned departments.

(Action: - PWD (B&R), HEWP Team)

Item No. 2/10: New modules in development

The Committee was informed about new modules (Dashboard of Project and Contract

Agreement, Bid Capacity, Milestone Based System and process for contractor actions) which

are under development on HEW Portal.

The Project Director presented the features of Dashboard of Project and Contract

Agreement, the Chairman directed that the dashboards may be implemented within 30 days

so that departments may refer these dashboards for monitoring and meetings purpose from

1st April, 2025 onwards.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Project Director informed that module of Milestone-Based System is in the final stage of completion and will be made live soon. The Chairman suggested that milestone tracking should be in indicative format in the beginning.

The Chief Engineer, Haryana Police Housing Corporation, pointed out discrepancy regarding the term "10% (ten percent) of the value of the balance work (amount of uncompleted work)" mentioned in Section 3, Part-I D. Cost Control, Clause 49.1 (Liquidated Damages) and term "10 (Ten) per cent of the contract price" mentioned in Section 3, Part-II, Contract Data to General Condition of Contract, Clause 17 (c) to impose the liquidated damages on basis of Milestone dates. It was decided to replace the term "balance work (amount of uncompleted work)" with "Contract Price" in the Clause 49.1 of the CBD and necessary amendment in the CBD would be done. The Project Director clarified that concerned departments may provide relaxation, if necessary, by mentioning suitable amendments under Clause 39.1 of CBD.

(Action: - PWD (B&R), HEWP Team)

Item No. 2/11: Impact of offline bill processing on work closure, bid capacity and scoring

The Committee was informed that several Departments are still processing contractor bills offline instead of using the online billing system through HEWP. The offline billing is causing impact on 'Scoring of Works' and 'Bid Capacity'. It was decided to stop the offline billing system and all future bills may be processed through HEWP.

The Chief Engineer, Haryana Police Housing Corporation informed the Committee that due to the absence of Secured Advance provision on HEW Portal, they are unable to start e-MB/Billing. The Project Director informed that this provision is currently not available but will be examined.

HPGCL and DHBVNL raised the issue to make the provision of Splitting of MB & Bill against Single Work Order for Different Divisions before the Committee. The Project Director assured that this feature will be implemented after discussions with HPGCL and DHBVNL officials.

(Action: - All Govt. Organizations on-boarded on HEWP, HEWP Team)

Item No. 2/12: GST reimbursement bills

The Committee was informed that various departments are facing difficulties in processing GST reimbursement bills on HEWP. Contractors in PHED and Development & Panchayat



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Department have submitted representation to issue detailed instructions for hassle free processing of GST reimbursement bills on HEWP. To address this, the Project Director, HEWP, presented the Standard Operating Procedure (SOP) for processing of GST reimbursement bills of contractors on HEWP (Annexure-III) for consideration and approval. The Committee reviewed the SOP, and it was decided that draft SOP will be circulated to all members to submit their observations and comments within 7 days.

(Action: - All Govt. Organizations on-boarded on HEWP, HEWP Team)

Item No. 2/13: Ticket resolution status and training/feedback sessions on HEW Portal

This agenda item was presented for the information of Committee.

Item No. 2/14: Final bill submission time limit for contractors after expiry of agreement

It was informed to the Committee that several departments are facing issues because some contractors do not timely submit the final bill post expiry of the agreement time-limit, which impacts the timely scoring of works and, consequently, affects the bid capacity. Considering these challenges, the agenda was presented to the committee to establish fixed timelines for the submission of final bills. The Committee approved a 60-day deadline for final bill submission and contractors who fail to meet this deadline must apply for time extension of work through HEWP. Instructions regarding this will be issued to all departments.

(Action: - HEWP Team, All Govt. Organizations on-boarded on HEWP)

Other points discussed with the permission of the Chair:

1. It was proposed to add (*National Informatics Centre (NIC)*, *Quality Assurance Authority and Anti-Corruption Bureau*, *Haryana*) as members of the Steering Committee of PMU for HEWP. The Chairman directed that the proposal may be placed before the Apex Committee for approval by including in the agenda for Apex Committee meeting.

(Action: - HEWP Team)

2. It was proposed to add the new clauses in CBD regarding 'grant of Bonus to Contractor for early completion of work' and 'action against Contractor for failure to commence work'. The Chairman directed that the proposal may be placed before the Apex Committee for approval by including in the agenda for Apex Committee meeting.

(Action: - HEWP Team)



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



3. The Committee deliberated on the implementation of GIS for the works being executed through HEWP. The Chairman desired to explore the way forward on this and accordingly incorporate the agenda before the Apex Committee. The Chief Engineer, ULB proposed to integrate ULB GIS system through APIs. The Project Director assured to explore the integration of ULB GIS system with HEWP.

(Action: - HEWP Team)

The meeting ended with a vote of thanks to the Chair.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



mio-newp.pwa@my.gov.m

Annexure -I

Attendance (the members who participated physically) of 2nd Meeting of the Steering Committee of the Project Management Unit (PMU) of the Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP was held on 28.01.2025 at 11:00 AM under the Chairmanship of the Commissioner & Secretary to Govt. Haryana, PHED at the Conference Hall of the Office of Engineer-in-Chief, Haryana PHE Department, Bay No. 19-20, Sector-4, Panchkula.

S.	Name	Designation	Mobile No.
No.	Ch. Davandar Dahira	Engineer in Chief (LICE) DUED	0012610000
1.	Sh. Devender Dahiya	Engineer-in-Chief (HOD), PHED	9812619000
2.	Sh. Anil Kumar Dahiya	Engineer-in-Chief (Buildings)-cum-HOD, PWD (B&R)	9417702442
3.	Sh. Kuldeep Singh	Engineer-In-Chief, HSAMB	9813436336
4.	Sh. Rajiv Batish	Project Director, HEWP-cum-Chief Engineer (Rural), PHED	9872617131
5.	Sh. Yogesh Mehra	Chief Engineer, PWD (B&R)	9671111066
6.	Sh. Rakesh Goyal	Chief Engineer, Panchayati Raj	9416251703
7.	Sh. Ashok Rathee	Chief Engineer, ULB	9468188887
8.	Sh. Rajeev Sharma	Chief Engineer, Housing Board Haryana	9911768833
9.	Sh. Satish Sharma	Chief Engineer, HPHC	9416067465
10.	Sh. J.S. Nara	Chief Engineer, UHBVN	9416950002
11.	Sh. S.D. Sharma	Chief Engineer, MICADA	9416496304
12.	Sh. Arun Pandey	HOD (Engg.), HSIIDC	9814148436
13.	Sh. Romit Chugh	Superintending Engineer, PWD (B&R)	9215928090
14.	Sh. Vipin Kumar	Superintending Engineer, IWRD	9416418210
15.	Sh. Ashish Gupta	Superintending Engineer, HSAMB	9466047318
16.	Sh. Harish Chandra Pant	Superintending Engineer, UHBVN	9023726614
17.	Sh. Anant Sangwan	Superintending Engineer, HVPNL	9212520009
18.	Sh. Sanket Sharma	OSD to C&S, PHED-cum-Executive	9466744148
		Engineer, PHED	
19.	Sh. Varun Gupta	Executive Engineer, PWD (B&R)	9780187068
20.	Sh. Gaurav Anand	Executive Engineer, ULB	9779249515
21.	Sh. Raveesh Pratap	Executive Engineer, IWRD	7696953941
22.	Sh. Amit Rathee	Executive Engineer, HSVP	9711880411
23.	Sh. Rajesh Ninaniya	Executive Engineer (P&D), DHBVNL	9812452530
24.	Sh. Deepak Sharma	Executive Engineer, HVPNL	9316369290
25.	Sh. Parveen Dahiya	Executive Engineer, HPGCL	9355084688
26.	Sh. Munish Malhotra	Deputy General Manager, HSRDC	8427830773



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



27. Sh. Dhiraj Kumar Gupta **Executive Engineer, HPHC** 9417317730 Sh. Pardeep Gulati Senior Accounts Officer, HVPNL 9316369225 28. 29. Sh. Sunny Verma Manager (Engg.), HSIIDC 9466996116 30. Sh. Vikash Dhiman Assistant Director, HIRMI 9466477812 31. Sh. Chaman Lal Sub Divisional Engineer, HSSPP 9463653569 Sub Divisional Officer, IWRD 32. Sh. Pardeep Kumar 9896097715 33. Sh. Sudesh Kumar Sub Divisional Officer, MICADA 8568829007 34. Sh. Vikram Saini Assistant Engineer, HPGCL 9466885441 35. Sh. Ram Katara AEE (P&D), DHBVNL 8005723909 36. Ms. Jyoti Sharma Programmer, HSRDC 9646332165 37. Sh. Satish Gupta Consultant, Development & Panchayats 8176051653 38. Sh. Pankaj Kamboj Project Engineer, HEWP 9416550881 Sh. Harish Bhatia SEO, PWD (B&R) 39. 8283803804 40. Sh. Naveen Bansal SEO, PHED 9416680242 Sh. Sunil Kumar System Analyst, PHED 9888316152 41. 42. Sh. Vishal System Analyst, PWD (B&R) 9592030103 43. Sh. Kapil Ghai Program Manager (Training & Cap. 8427831363 Building), HEWP Sr. Consultant (Construction 44. Sh. Rohit Choudhary 9442596823 Management), HEWP



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula - 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Annexure -II

Attendance (the members who participated through Video Conferencing) of 2nd Meeting of the Steering Committee of the Project Management Unit (PMU) of the Haryana Engineering Works Portal (HEWP) to review the implementation of HEWP was held on 28.01.2025 at 11:00 AM under the Chairmanship of the Commissioner & Secretary to Govt. Haryana, PHED at the Conference Hall of the Office of Engineer-in-Chief, Haryana PHE Department, Bay No. 19-20, Sector-4, Panchkula.

S. No.	Name	Designation
1.	Sh. Vishal Bansal	Chief Engineer, FMDA
2.	Sh. Abhinav Verma	Executive Engineer, GMDA
3.	Sh. MM Arora	Project Associate, HEWP



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



Annexure -III

Subject: Standard Operating Procedure for processing of GST reimbursement bills of Contractors on Haryana Engineering Works Portal (HEWP).

It has come to the notice that various departments are facing difficulties in processing GST reimbursement bills on HEWP. Contractors in PHED and Dev & Panchayat Department have submitted representation to issue detailed instructions for hassle free processing of GST reimbursement bills on HEWP. A meeting was held on **02.01.2025 at 4:00 PM** under the chairmanship of worthy Engineer-in-Chief, PHED, Haryana, with various contractors of PHED to sort out the pending issues in this regard.

Accordingly, it has been decided to follow below mentioned steps for processing GST reimbursement bills on HEWP.

- Contractor to submit GST Invoice/Bill: The contractor shall submit duly signed copy of Tax Invoice in prescribed format as per CGST Rules/Act, 2017 containing details such as Date of Tax Invoice, Invoice Number, Total value/amount with GST amount, Tender ID, Name of division, HSN Code. The invoice/data shall be uploaded to HEW Portal.
- 2. **Additional Documents**: The contractor shall mandatorily provide following GST related documents of the previous month and will upload on HEWP:
 - 1) GSTR-1
 - 2) GSTR-2B,
 - 3) GSTR-3B,
 - 4) Statement of TDS return (GST) accepted by contractor against filing of GSTR-7 by the department.
 - 5) Copy of the challan/transaction ID/CPIN confirming GST payment from the GST portal (if applicable).
- 3. **Contractor shall submit Undertaking**: The contractor shall mandatorily upload the self-attested undertaking specified below on HEWP:
 - 1) The GST amount mentioned in the invoice is included in GSTR-1 and will not be altered in the future.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



- 2) The Input Tax Credit (ITC) which have appeared in GSTR-2B and claimed in GSTR-3B relates to eligible ITC and particularly related to such services which are provided to the department for allotted work.
- 3) The copy of TDS return for the month which is accepted by contractor against filing of GSTR-7 by the department (Statement of deduction of TDS GST) for the work against which GST reimbursement is being claimed.
- 4) If any amendments are found in the submitted returns, the contractor will be held responsible, and necessary action will be taken.
- 5) That complete and accurate documentation has been submitted.
- 4. **Contractor shall submit GST calculations**: Contractor to submit calculations and will upload on HEWP for settlement of liability and proof of payment of GST by contractor for previous month:

S. No.	Description	Amount	
1	GST Payable as given in GSTR-1	Α	
2	Less: Amount of Input Tax Credit as provided in GSTR- 2B or claimed in GSTR-3B (whichever is lower)	В	
3	Less: Amount of Input Tax Credit available in 'C' electronic cash ledger (opening balance)	С	
4	Net GST Payable	D = (A-B-C)	
5	Amount for which Challan Paid/Transaction ID/CPIN	Е	
6	Difference *(it should be zero "0" or negative)	F*= (D-E) *(it should be zero "0" or negative)	

5. **Department to check following Documents**:

1.) The verification of the GSTIN on the invoice shall be carried by department visiting the GST portal (https://www.gst.gov.in/). Use the "Search Taxpayer" option and enter the GSTIN to check if it is valid.



PUBLIC HEALTH ENGINEERING DEPARTMENT

Bays No. 13-18, Sector 4, Panchkula – 134112 Website: https://works.haryana.gov.in Phone Number: 0172-2566393 Email: info-hewp.pwd@hry.gov.in



- HSN/SAC Code: Department shall verify the HSN (Harmonized System of Nomenclature) code or SAC (Service Account Code) of GST mentioned on the invoice.
- 3.) **B2C Transactions**: Department shall check the value of 'Business to Consumer' (B2C) transactions using the contractor's GSTR-1. The value in GSTR-1 should be equal or more than the supplies made to Concerned Department for that particular month.
- 4.) Statement of TDS return charged on GST head, of the contractor for the previous month: To check, whether the contractor has included the GST-TDS deducted for this work in the TDS return for the previous month's bill payment.
- 5.) **GST Calculations:** GST Payable as given in GSTR-1, Less: Amount of Input Tax Credit as provided in GSTR-2B, Net GST Payable, Amount for which Challan Paid. It must be ensured that difference should be zero "0" in the previous month for the GST reimbursement bill.

Executive Engineers to process reimbursement of GST Bills after checking above details and ensuring compliance to Common Bid Document (CBD) and GST rules. The reimbursement of GST will only be processed if all CBD conditions and legal requirements have been duly complied.
